


Jal Sanchay Abhiyan

Delhi Development Authority


BAMNOLI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II, 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Pitching-100%,Footpath Repair-50%, Boundary Wall Repair-100% Plaster-100%, Painting-0% Work is held up due to rain

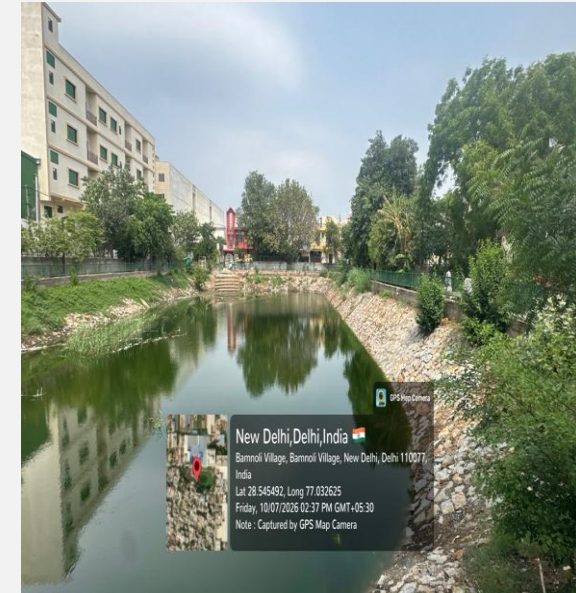

HASANPUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II ,8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Work has been awarded.The work is likley to be completed by November 2026.

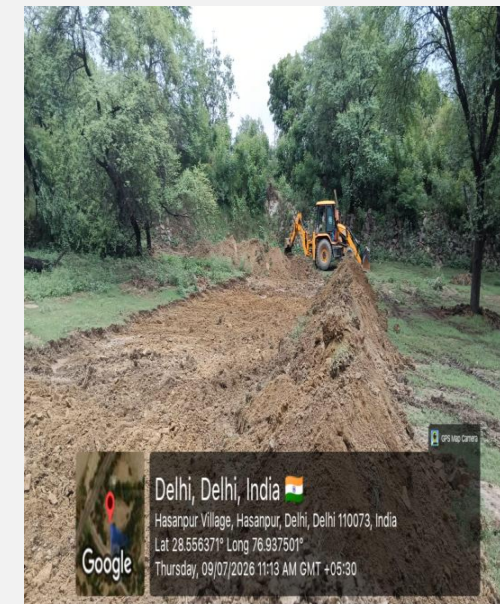

JHARODA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- The work is under tendering process and is likly to be awarded within 15 days




KHAR KHARI RONDH

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Work has been awarded. The work is likley to be completed by November 2026.






TIKARI KALAN

- District: West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Work has been awarded. The work is likely to be completed by November 2026.

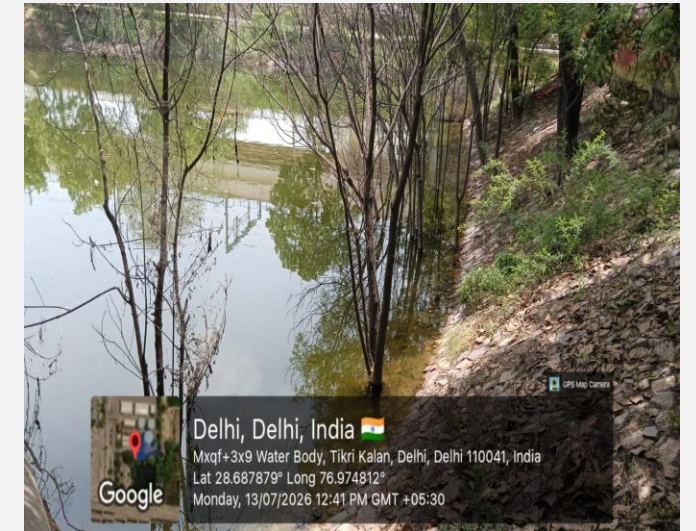

CHAWALA

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Work has been awarded. The work is likely to be completed by November 2026.

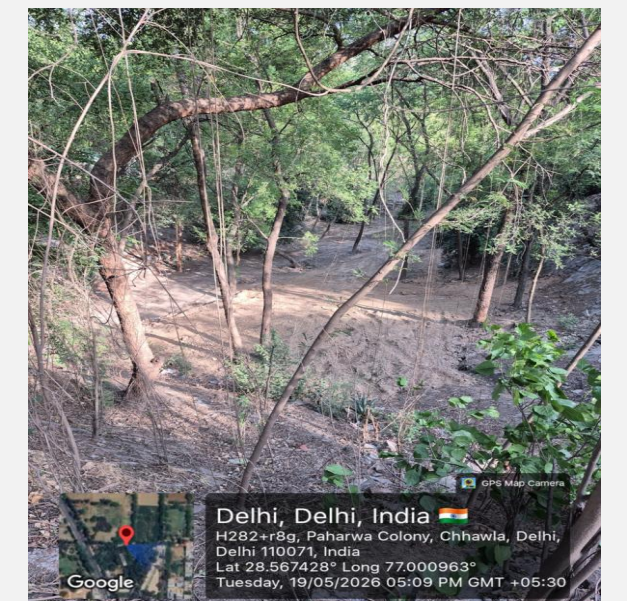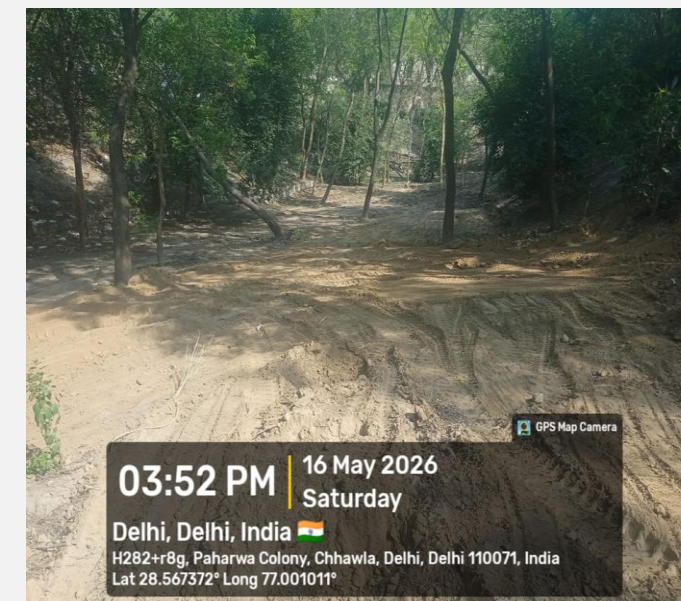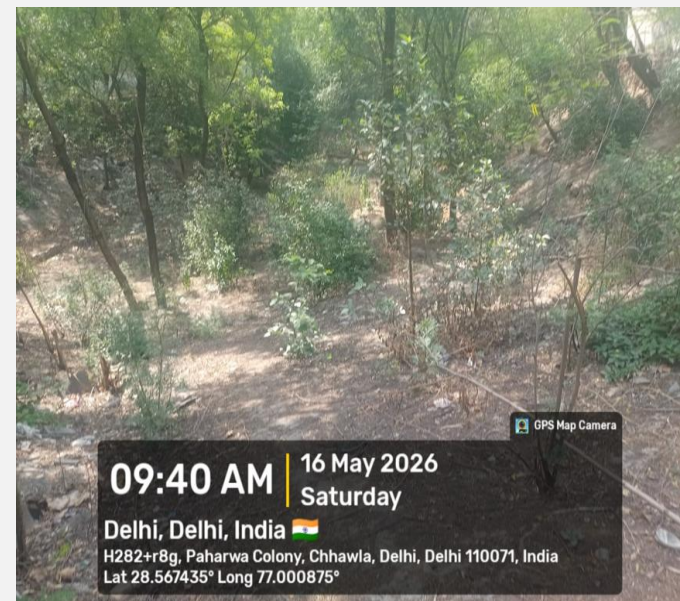


CHAWALA

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Work has been awarded. The work is likely to be completed by November 2026.




PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.

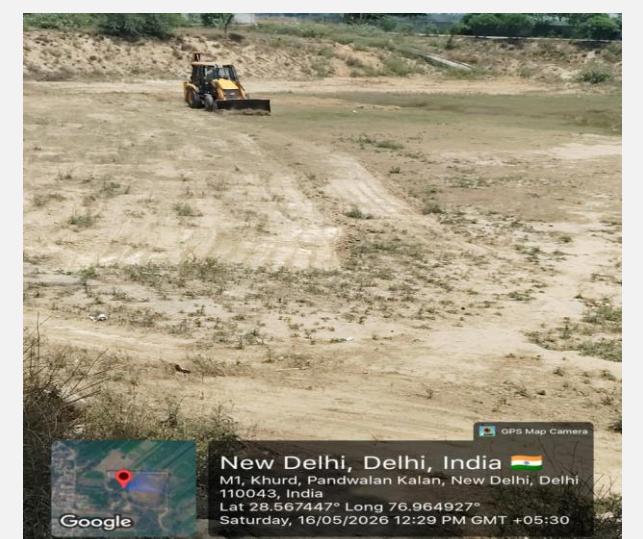


PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Work has been awarded. The work is likely to be completed by November 2026

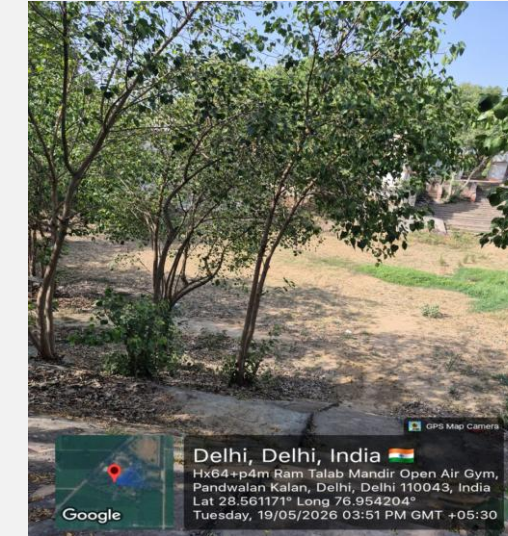

PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.

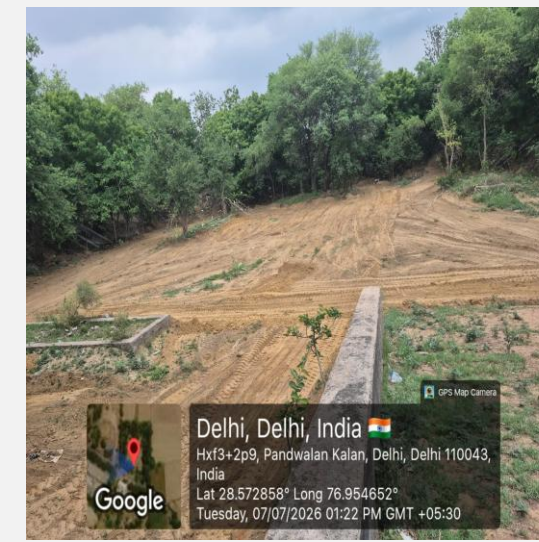


JHUL JHULI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.





JHUL JHULI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.

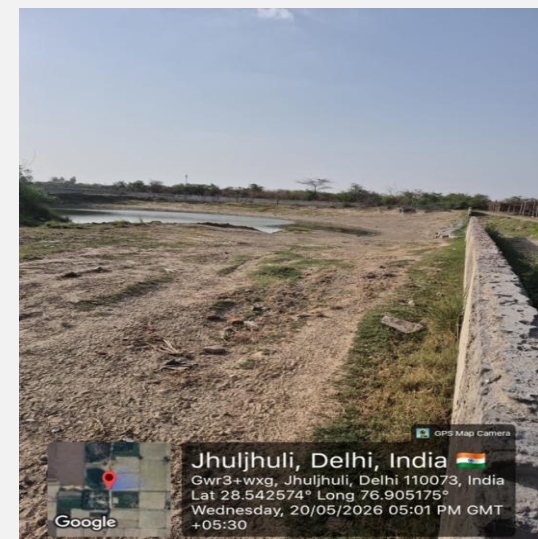



QAJIPUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.

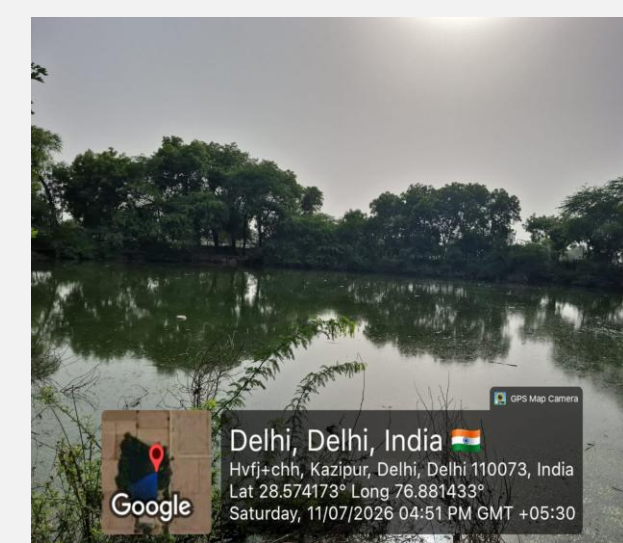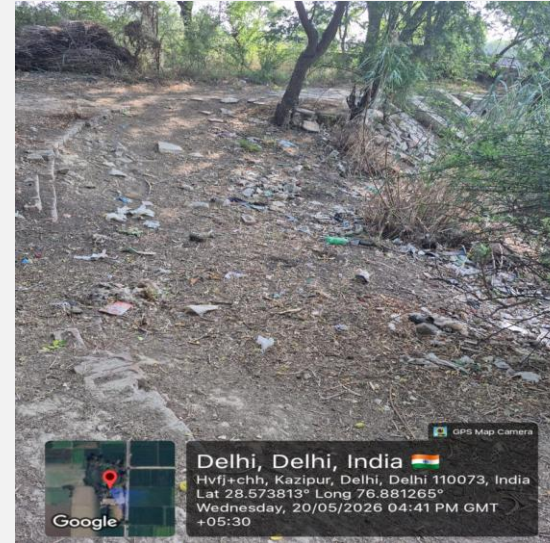


REWLA KHAN PUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- The work is in award stage and is likely to be start within 15 days .The expected completion is february 2027.

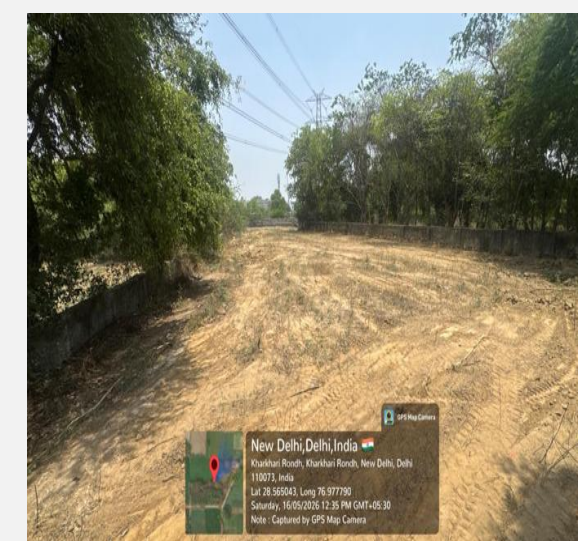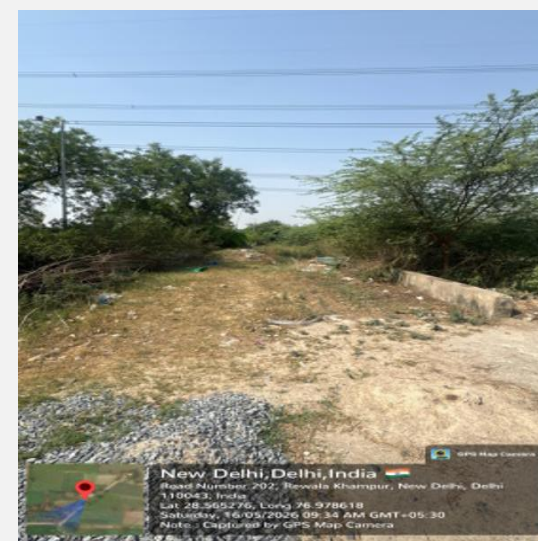




BAPROLA

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated.The Work (Fencing /signage board) will be completed by 31 oct 2026.

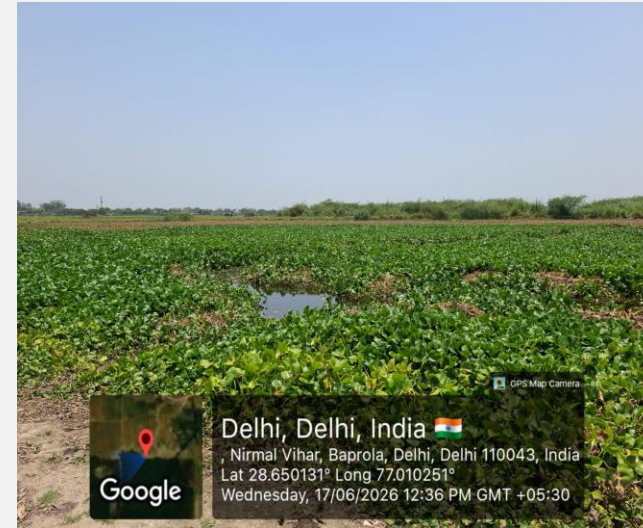


KAMRUDIN NAGAR

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is in progress.
- Phase -2 work :- Tender has been floated.Work (Repair maintenance)will be completed by 31 March 2027

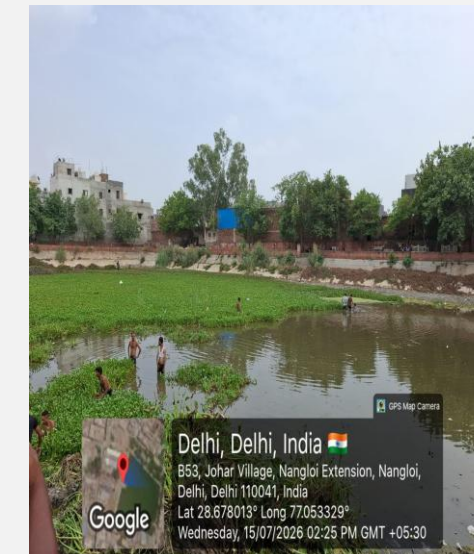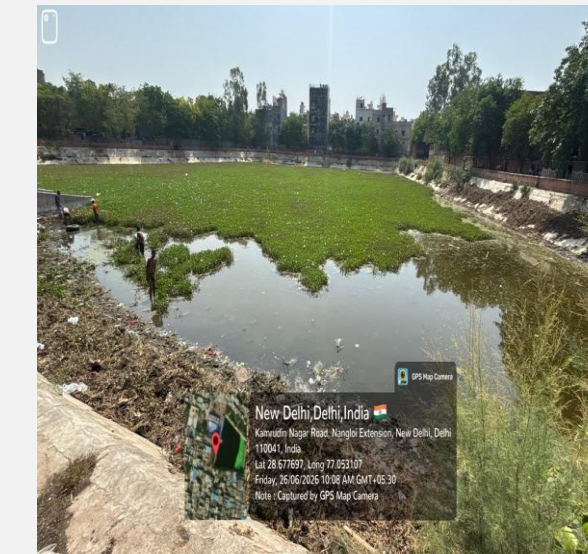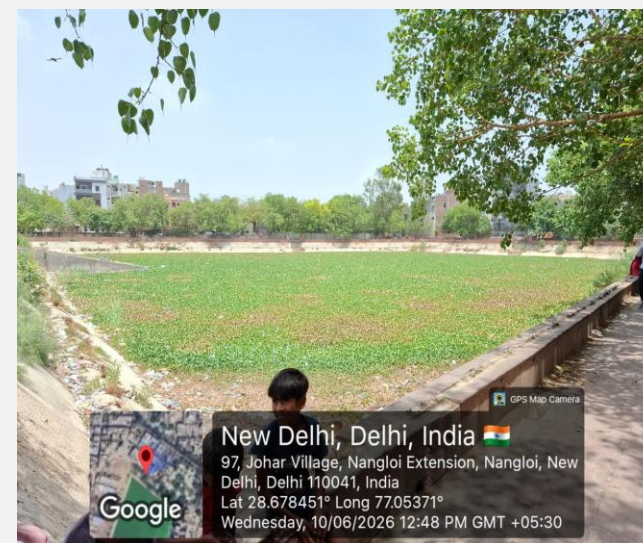


MUNDKA KHASRA NO. 178/1

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated. Work for 2nd phase (Pitching, footpath, Boundary wall etc) will be completed by 31 March 2027

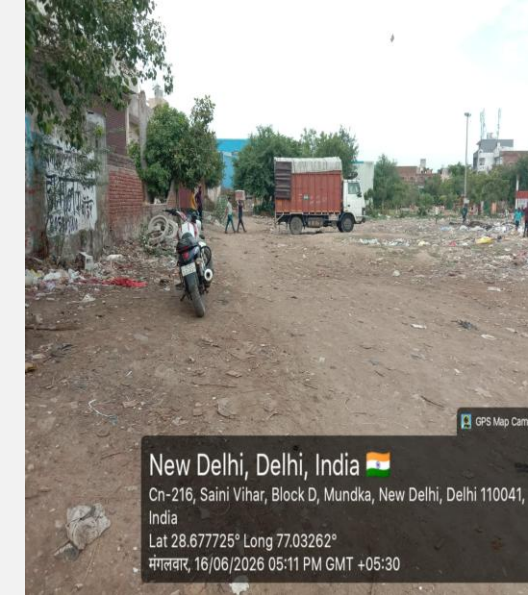

BAKKARWALA KH NO. 83

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Work for 2nd phase (Pitching, footpath, Boundary wall etc) is under tendering process & will be completed by 31 March 2027

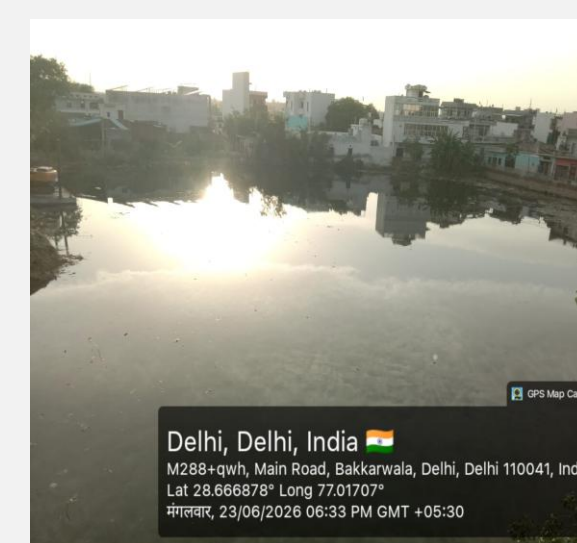



BAKKARWALA KH NO. 82

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated. Work for 2nd phase (Pitching, footpath, Boundary wall etc) will be completed by 31 March 2027





HASTSAL KH. NO. 55/16 & 55/17

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tendering process is in progress. (Pitching, footpath, Boundary wall etc). The timeline for completion of work is 31 March 2027.

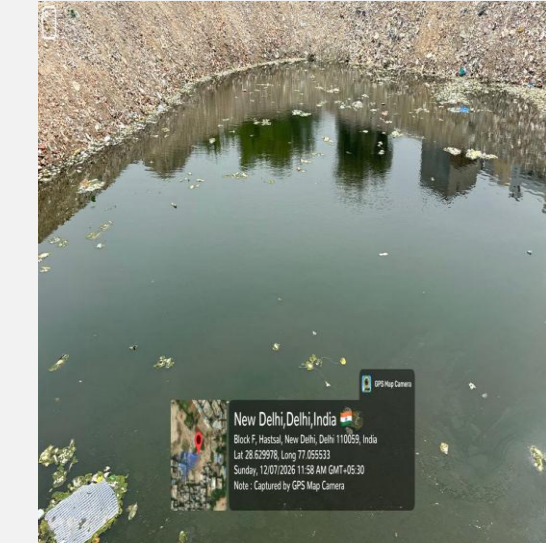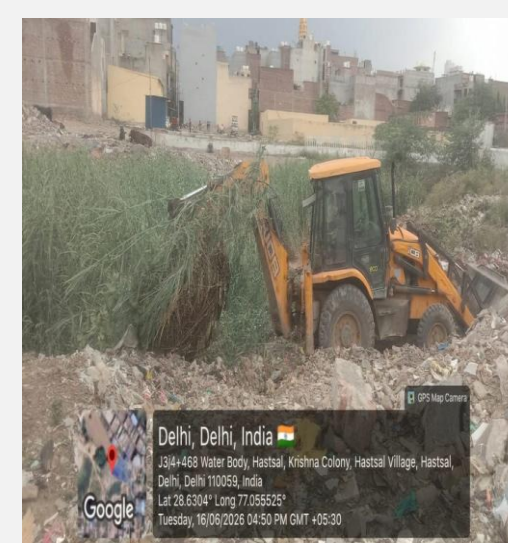



BAPROLA(23//17,23//24,23//25,29//4)

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated.Work (Repair maintenance)will be completed by 31 Dec 2026

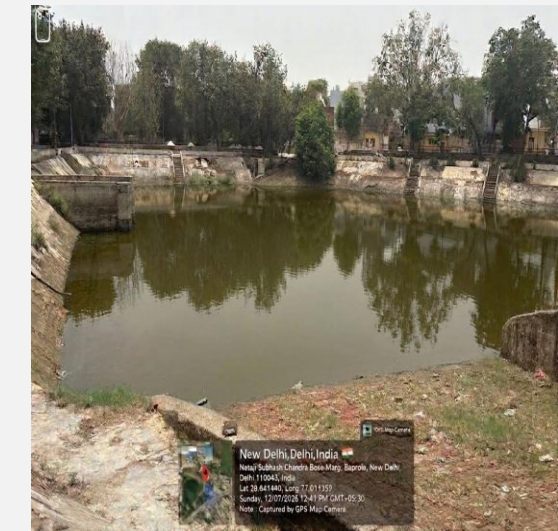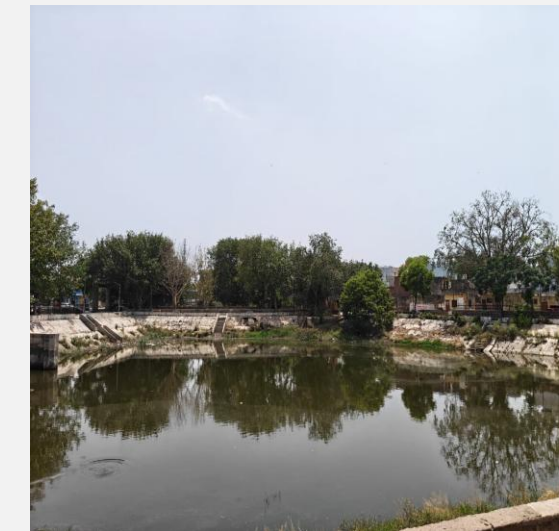

DEENDARPUR(338)/(1087/234)

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- During execution, the water body was submerged due to continuous inflow from the PWD drain and rainwater.As MCD drain work is ongoing, the water body is being utilized for wastewater diversion to prevent flooding of nearby areas. Accordingly, the rejuvenation work has been kept in abeyance.
- Phase-II work :- The tender for phase -2 work (Repair and maintenance) work has been uploaded.

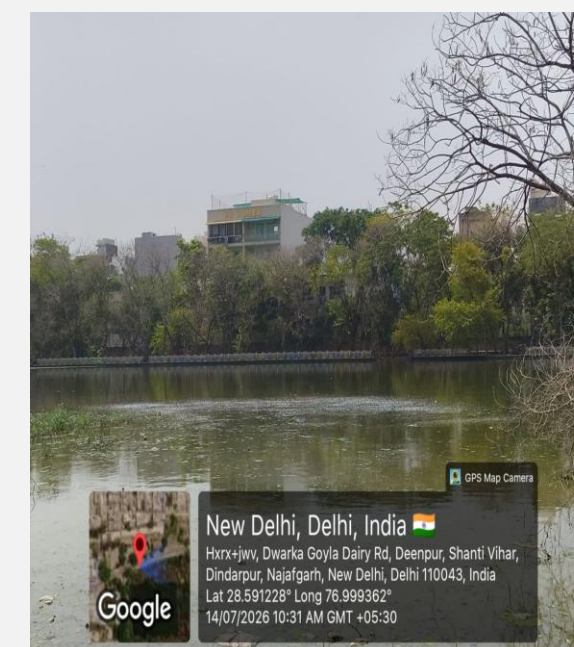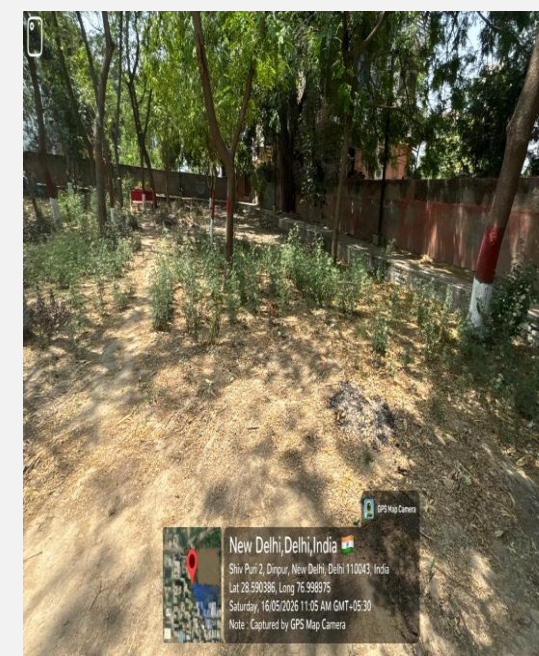



RAJPUR KHURD KH. NO 38

- District: South East
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026



MAIDANGARHI KH. NO. 554/2

- District: South
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026

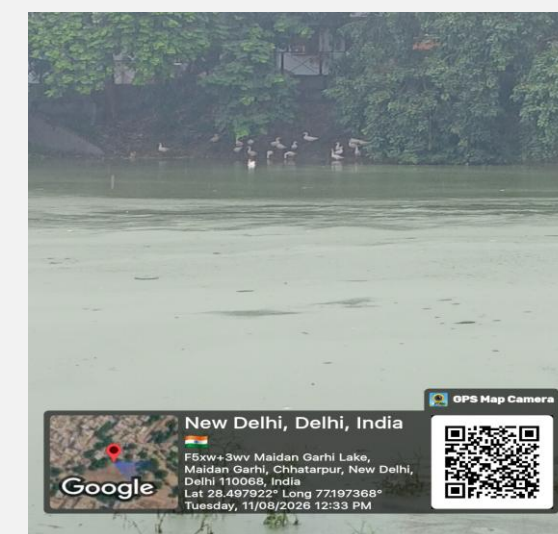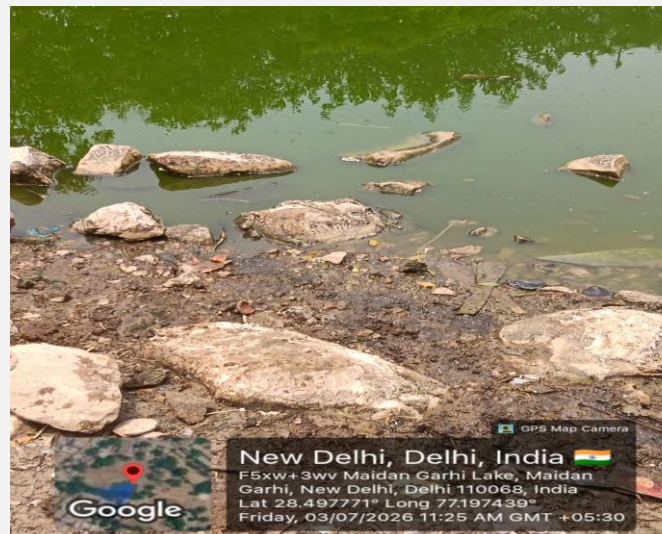


KISHANGARH KH. NO. 1166, 1167, 1168,109,1219

- District: South
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026




SANJAY LAKE, MAYURVIHAR

- District: East
- Concerned Officer: Sh. Saurabh Mishra EE/HCD-2 M- 7054520525
- Phase-I- Phase I is completed
- Phase-II- ARMO and TS has been issued .Tender is in process.

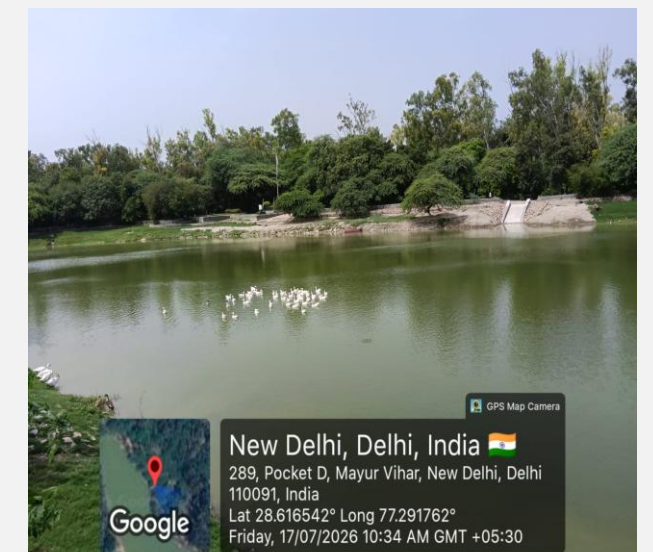


RANGPURI 660(12-12)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- No Work Required in Phase-II

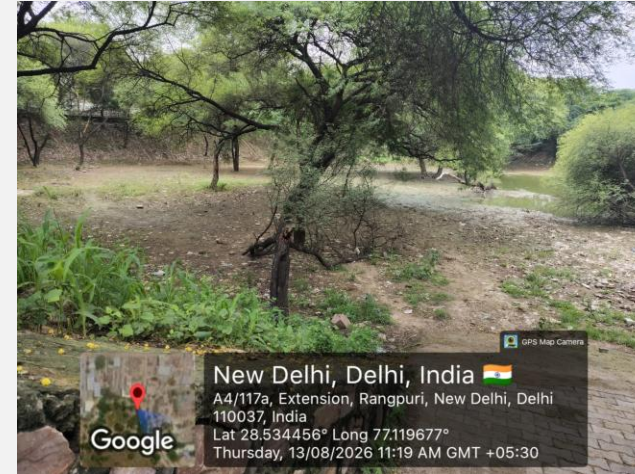

KAPASHERA KH NO. 664/1

- District: South West
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.




MAHIPAL PUR F/90 KH NO. 1030

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.



RAJOKARI KH NO. 41

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.

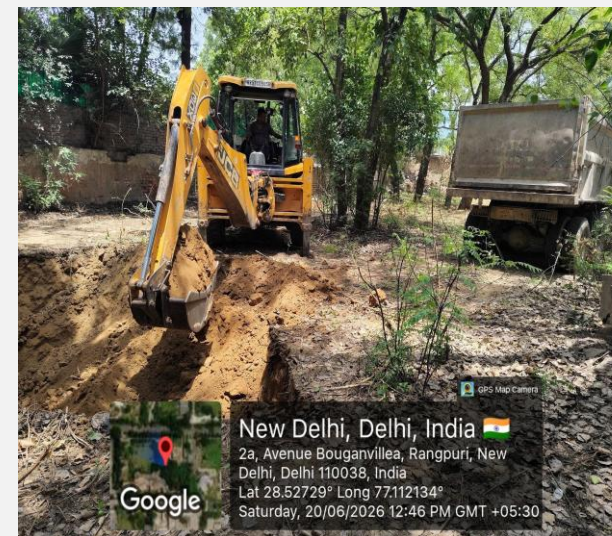


RAJOKARI KH NO. 848

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.



RAJOKARI KH NO. 695

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.

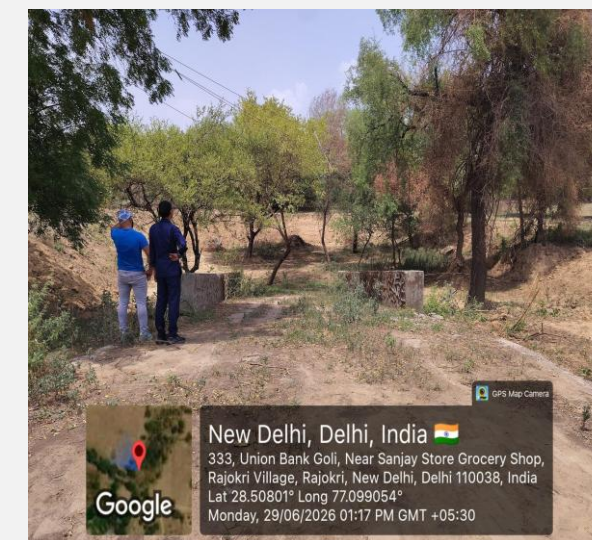

MADANGIR KH. NO. 191-MIN

- District: South
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Minor works of repair of boundary wall, track etc is under taken in the phase-I work and under process, the timeline for completion of work is 31.12.2026.




GHITORNI 437(17-19)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II-The A/A and E/S for the 75 KLD STP work is in progress.



RANGPURI 105(6-9)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Tender uploaded and the timeline for completion of work is 31.12.2026.

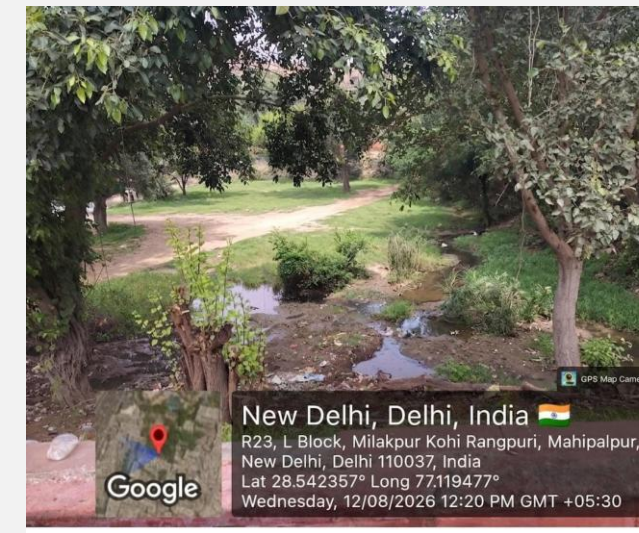


KATEWARA KH. NO. 473, 474, 477, 478, 479, 481

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- completed
- Phase-II- work started w.r.t Construction of Boundary wall, Red sand stone flooring in Steps further Toe wall, Linning, footpath will be completed by 31.12.26.





SULTANPUR DABAS KH. NO. 35/37

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 ,9213200667
- Phase-I- work has already been completed
- Phase-II- civil repair work has been started and the same will be completed by 15.10.26.

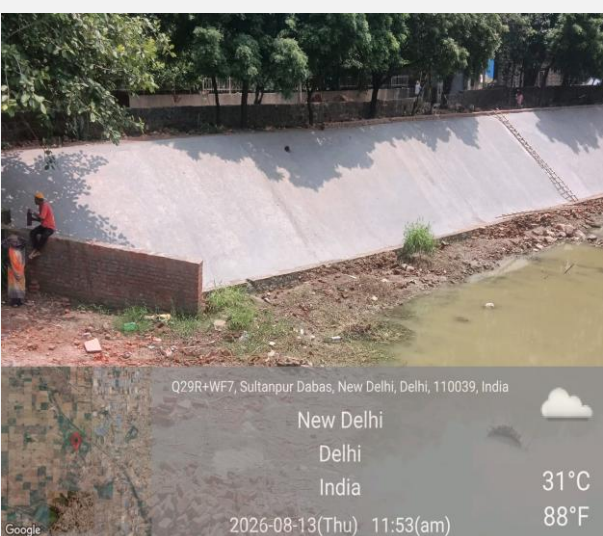




Rani Khera Kh. No. 74/2

- District: Outer North
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3, 9971154443
- Phase-I- Phase -I completed
- Phase-II- Phase -II completed

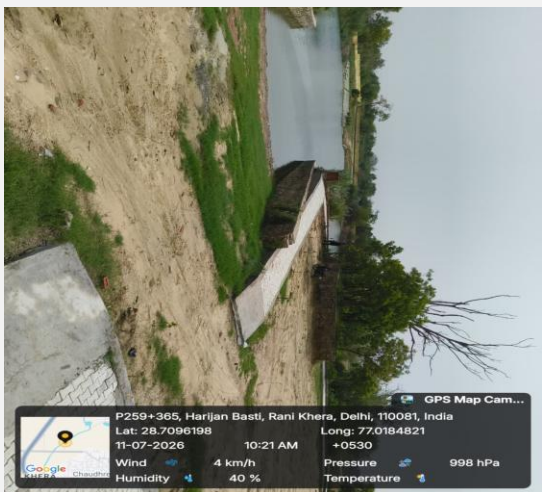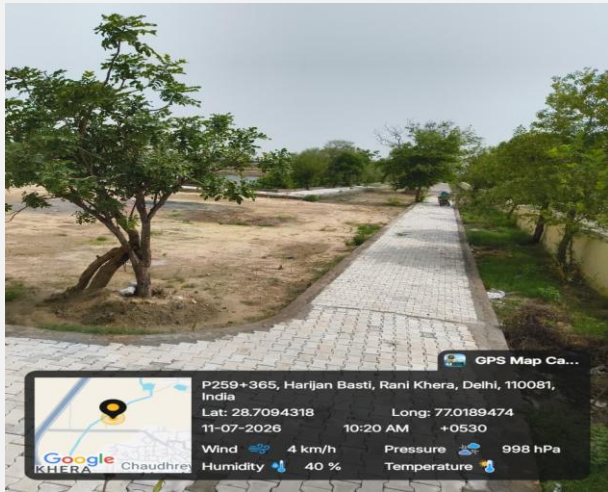


RANI KHERA KH. NO. 9/23 AND 9/17

- District: Outer North
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- Phase -I completed
- Phase-II- Phase -II completed

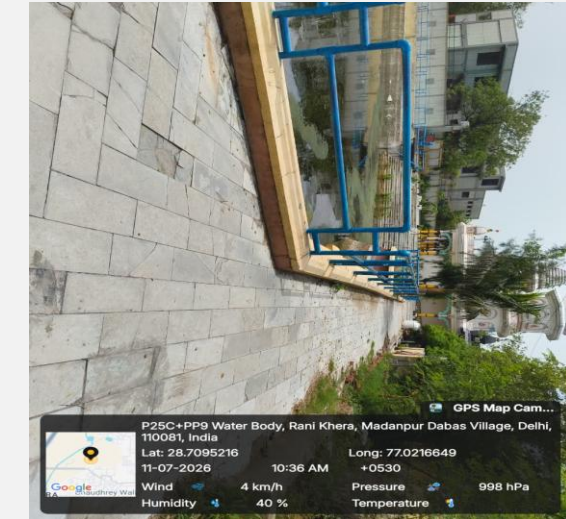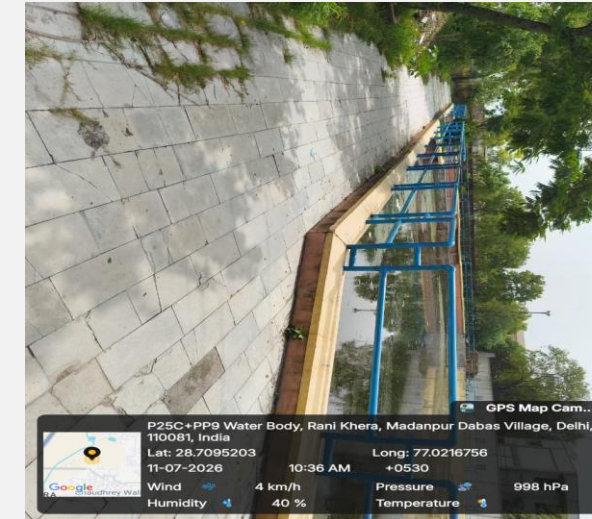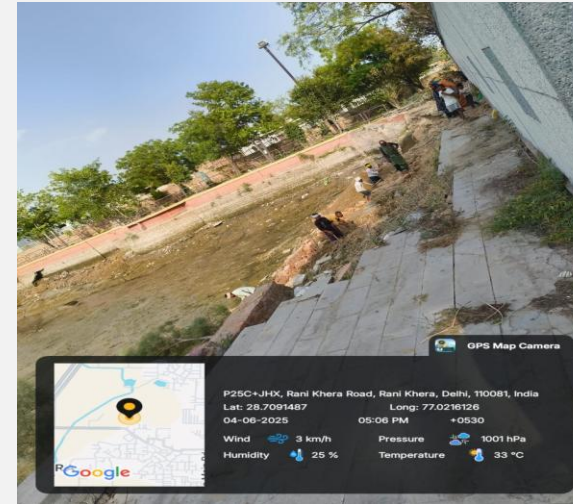

MADANPUR DABAS KH NO. 76

- District: Outer North
- Concerned Officer: Sh.Amit Kumar, EE/RMD-2, M-8178791202
- Phase-I- For Phase-I Cleaning of weeds, scrubs vegetations, Prepration of slope, Jungle cleaning and desilting of water body is completed.
- Phase-II- repair of foothpath, boundary wall and side slopes is under progress and will be completed on 30.09.2026.

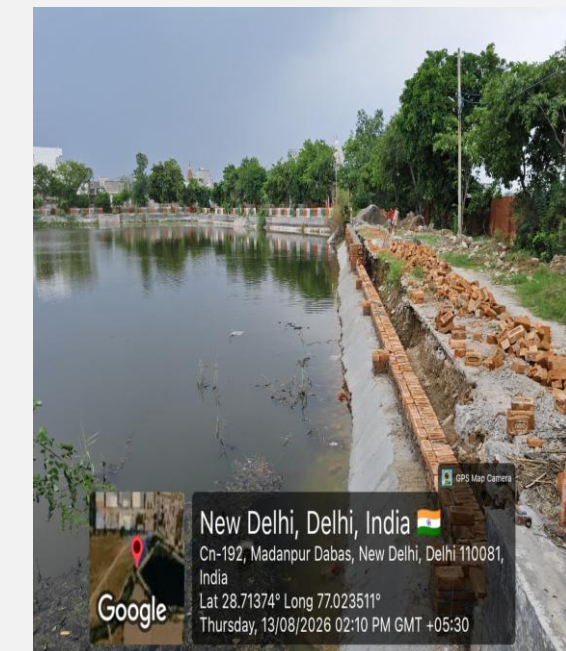

NANGAL THAKRAN KH. NO. 92 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work started w.r.t Repair of Boundary wall, Red sand stone wall cladding further Toe wall, Linning, footpath will be completed by 31.12.26.



NANGAL THAKRAN KH. NO. 87 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.



CHANDPUR KH. NO. 32/10

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work has been completed
- Phase-II- civil repair work of pitching, boundary wall , footpath work is in progress and dewatering of water body is in progress for lining work and the same will be completed by 20.10.26.



Budhanpur Mazra Kh. No. 36/7, 36/8

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work is in progress and the same will be completed by 31.10.26.




JATKHORE KH. NO. 35/25 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- Work is completed due time.
- Phase-II- work is in progress and the same will be completed by 30.11.26.




BUDHANPUR MAZRA KHASRA NO 36/10/1

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed. Civil work will start as soon as the rain intensity will diminish.
- Phase-II- work is in progress and the same will be completed by 31.10.26



BAWANA KHASRA NO 108/25

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed.
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.

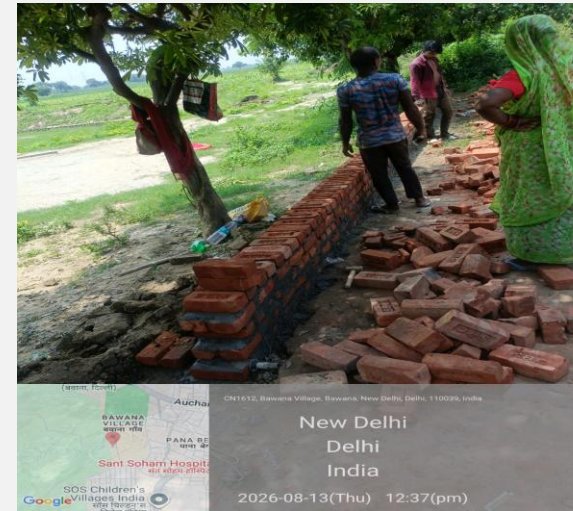

KATEWARA KH NO 824

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed.
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.



GARHI RANDHALA

- District: North West
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- The works under Phase-I is completed
- Phase-II- the tender is in progress with a target date of 31.12.2026




GARHI RANDHALA

- District: North West
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- The works under Phase-I is completed
- Phase-II- the tender is in progress with a target date of 31.12.2026





SAWDA

- District: North-west
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3
9971154443
- Phase-I- The works under Phase-I is completed.
- Phase-II- Work is in progress (total progress 20%) and likely to be completed by 30.10.2026

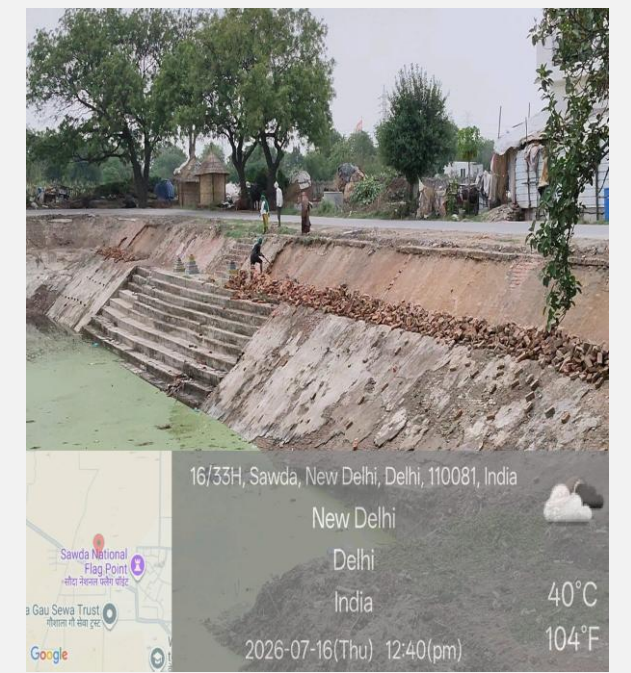


NITHARI

- District: North-west
- Concerned Officer: Sh.Amit Kumar, EE/RMD-2
- Contact No. 8178791202
- Phase-I- For Phase-I Cleaning of weeds, scrubs vegetations, Jungle cleaning and desilting of water body is .
- Phase-II- Work held up due to flooding.

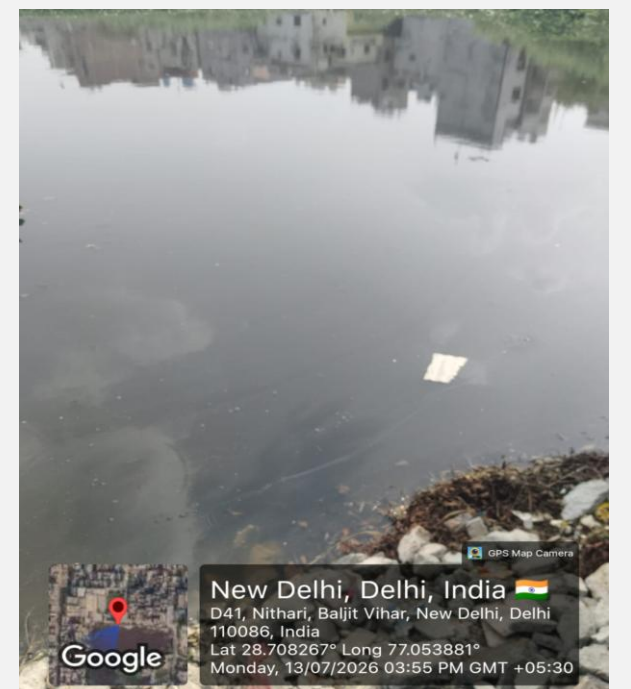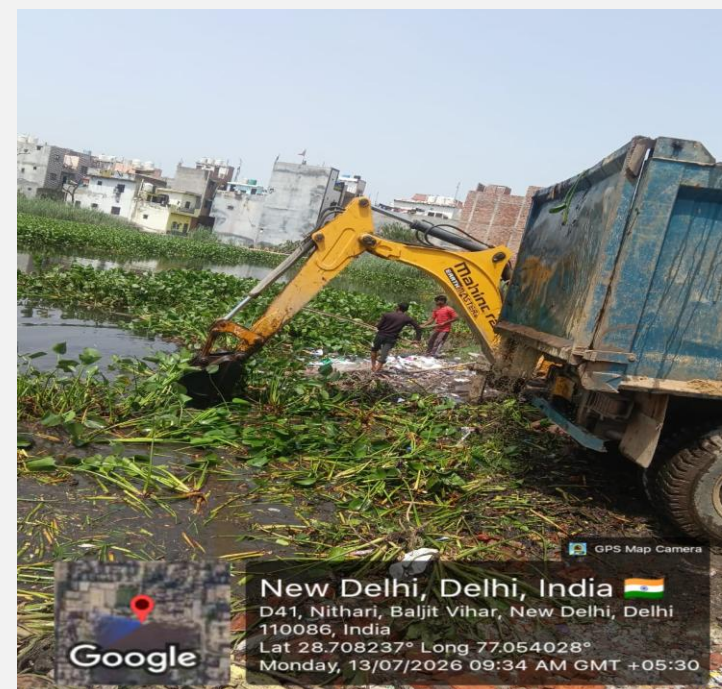

BANKNER

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

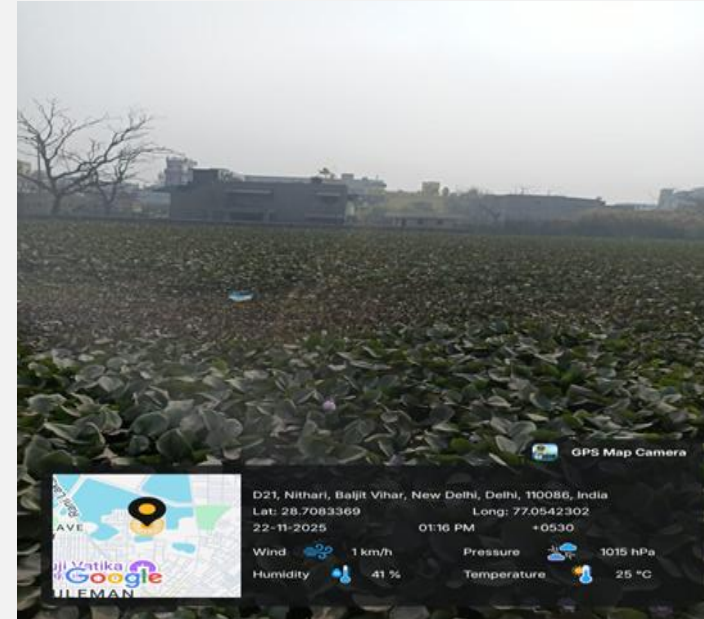

BANKNER

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.



MAMMOORPUR

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.




TIKRI KHURD

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.




TIKRI KHURD

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

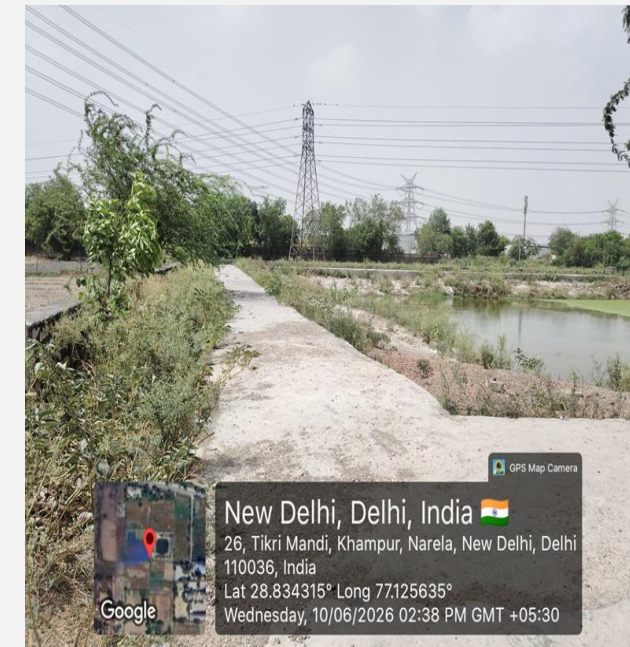



LAM PUR

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

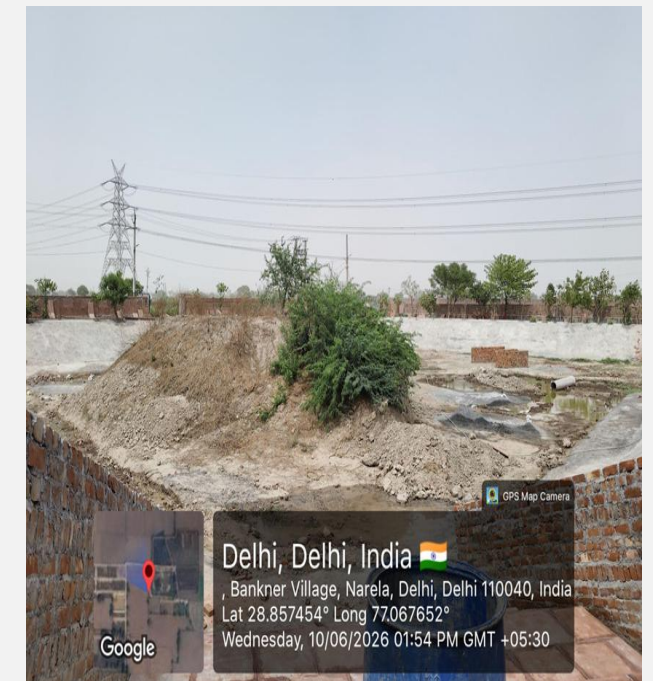

AKBARPUR MAJRA

- District: North West
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I has been Completed
- Phase-II- The work is in progress

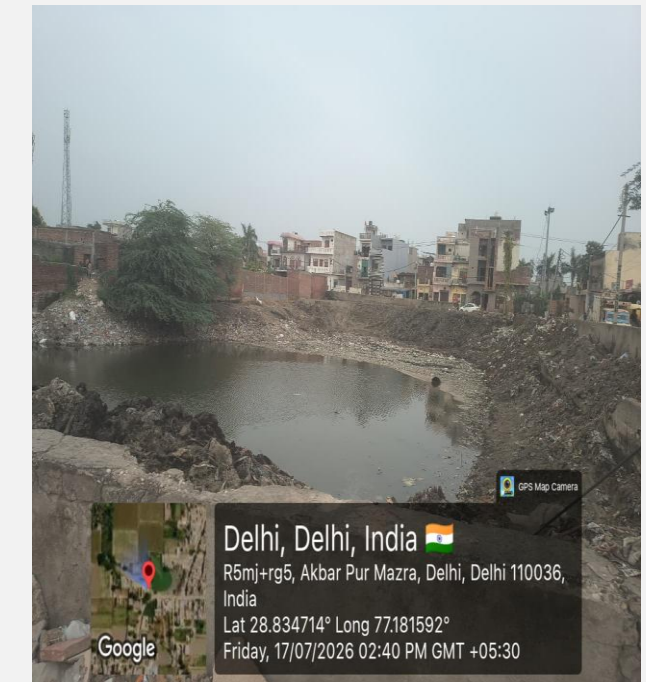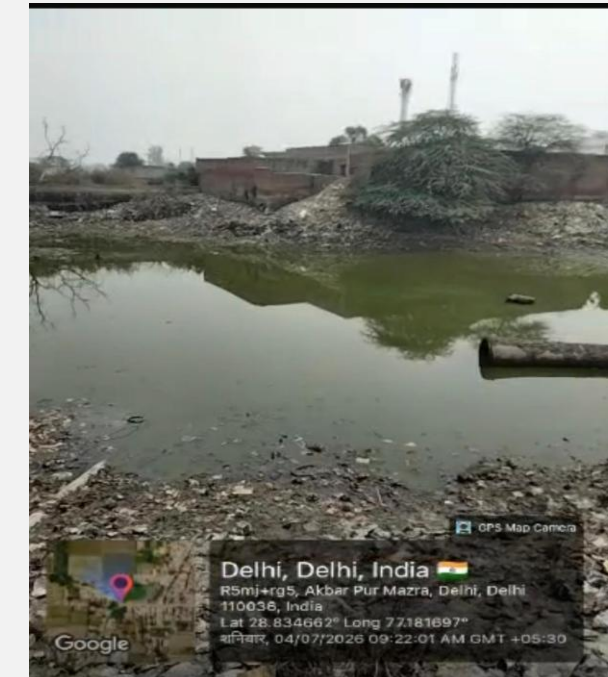


ALIPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- The work is in progress



BAKHTAWAR PUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- The work of phase II is in progress

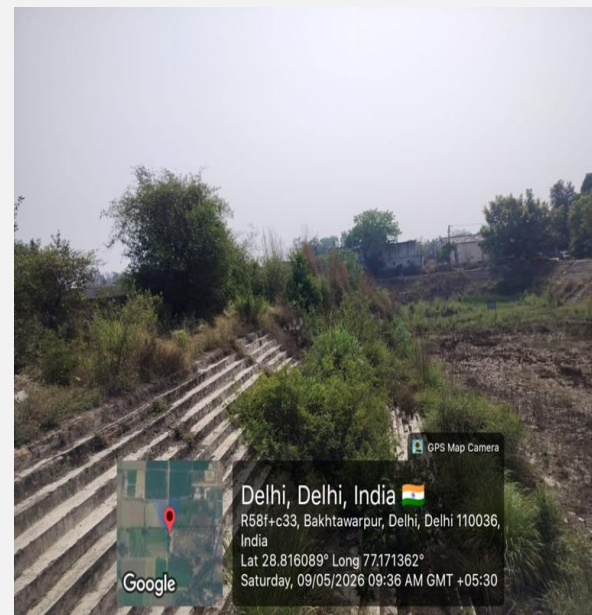


BAKHTAWAR PUR

- District: : North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- The work of phase II is in progress



BUDHPUR BIZAPUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress

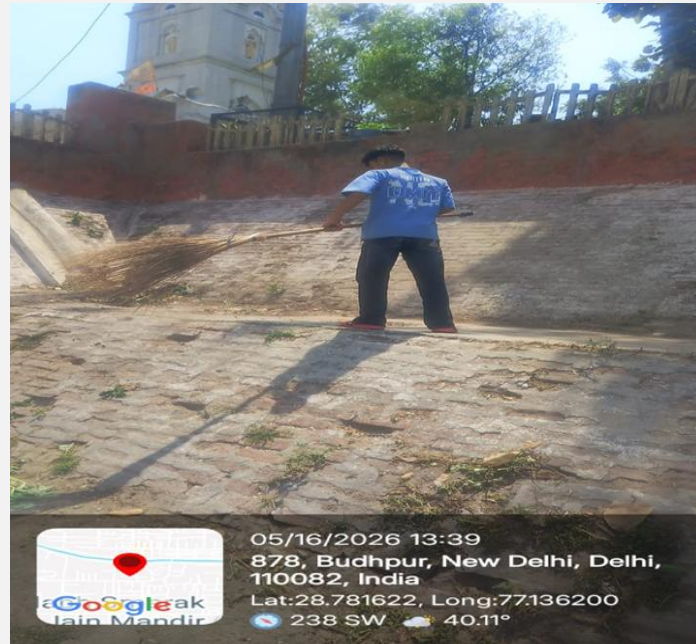


HIRANKI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress



HIRANKI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work of Phase -I has been completed
- Phase-II- Work is in progress.

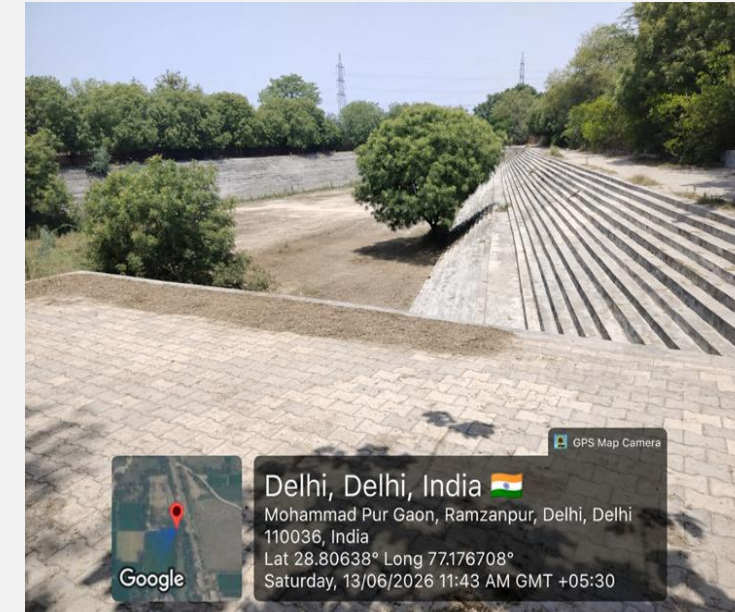

IBRAHIMPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress.



KHERA KALAN

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress




NANGLI PUNA

- District: North West
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress




SAMAY PUR F/90

- District: Central
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Work is in progress

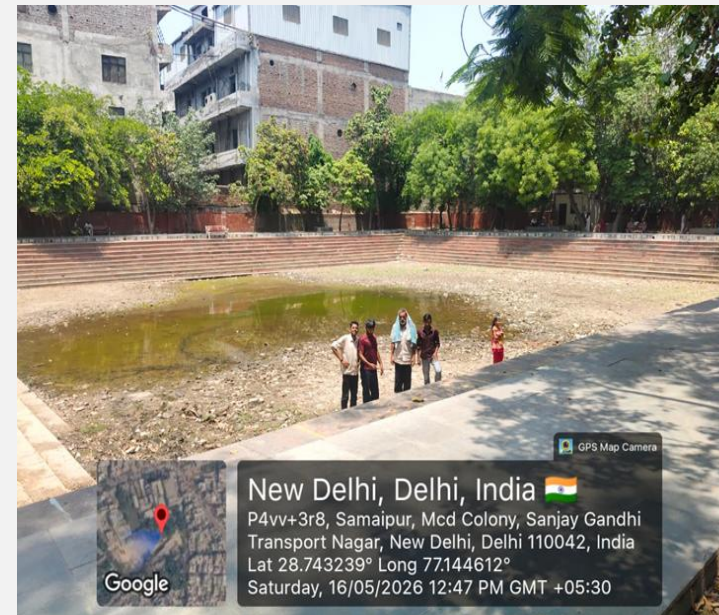


SIRASPUR

- District: Central
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- hase-I- The work for Phase-I has been Completed
- Phase-II- VWork is in progress

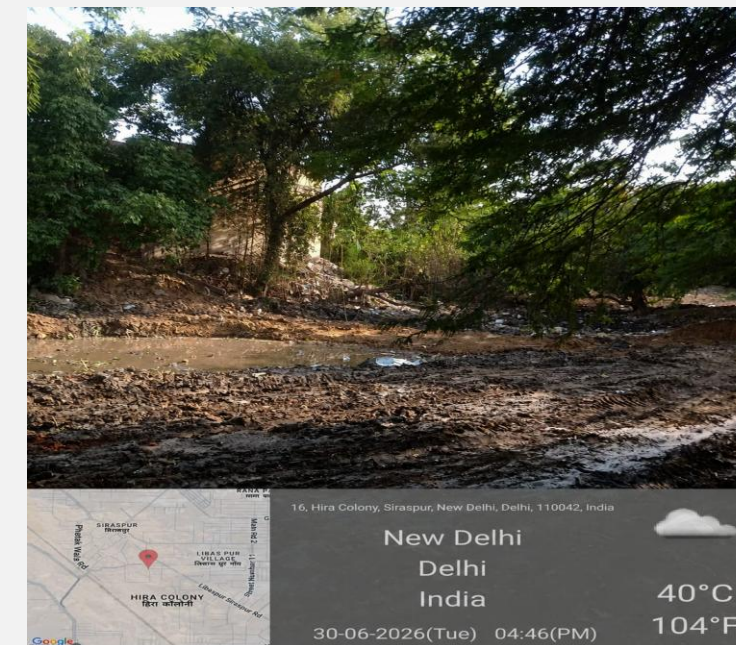


TIGI PUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed for Phase-I
- Phase-II- Work has been completed for Phase-2.

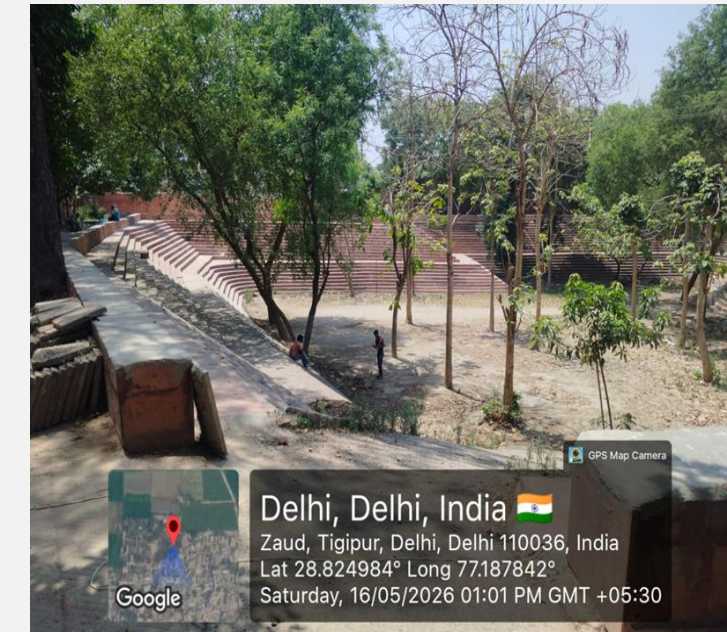

SAHIPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed.
- Phase-II- Next week vacant land will be handed over to Horticulture wing for Landscaping

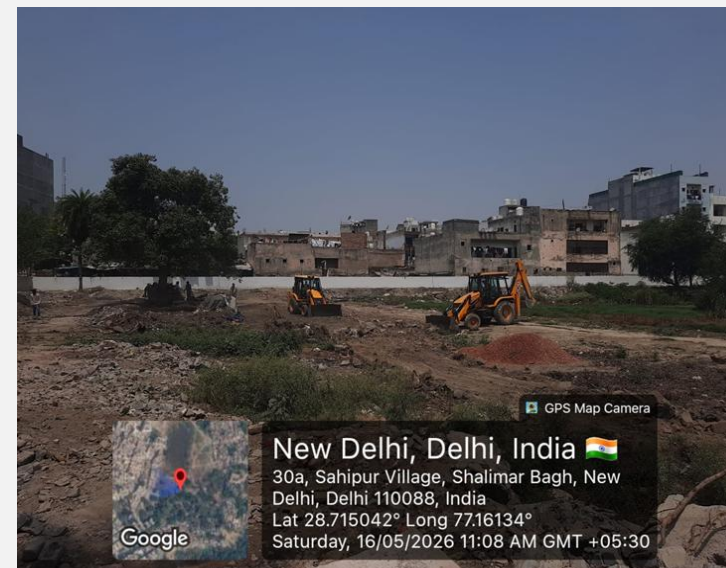

BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I has been Completed
- Phase-II- work is in progress



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District : North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- phase 2 is in progress



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work for Phase-I in tendering process.
- Phase-II- Tender at acceptance stage



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: Central
- Concerned Officer: : Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- Work has been completed
- Phase-II- phase 2 is in progress






BAKHTAWAR PUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is completed
- Phase-II- Phase-II Work: The work awarded on 21.08.2026. The site has been shown to the agency, and the agency has been instructed to urgently mobilize the required manpower and machinery to commence the work. Work has been started at Site.





SHAHBAD MOHD.PUR F/03, (NEAR RAILWAY FATAK)

- District: New Delhi
- Concerned Officer: Sh. Vishal Kumawat EE/HCD-7 9759835794
- Phase-I- Phase-I work is completed
- Phase-II- Phase -2 work :- The work awarded on 21.08.2026. The site has been shown to the agency, and the agency has been instructed to urgently mobilize the required manpower and machinery to commence the work.

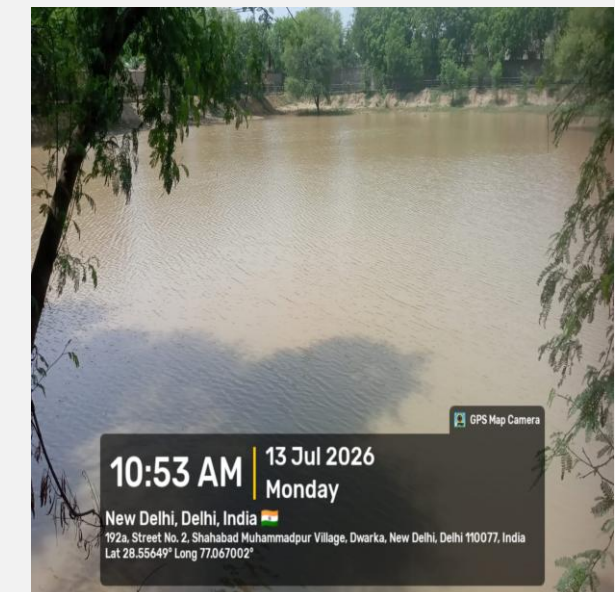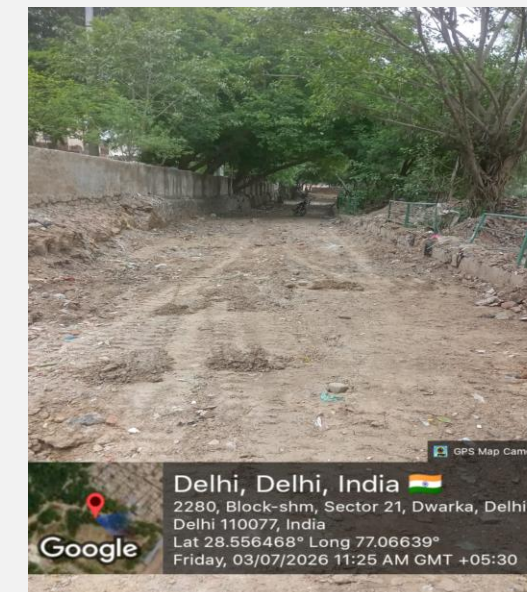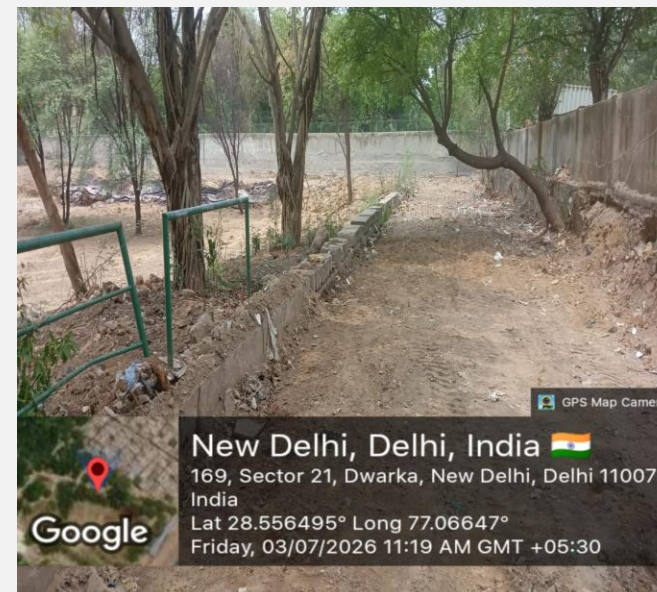




GARHIPEERAN F/89 @ PEERAGARHI (PARK AND LAKE AT DISTRICT PARK, PASCHIM VIHAR)

- District: West
- Concerned Officer : Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed.
- Phase-II- work such as fencing and already exist at waterbody.

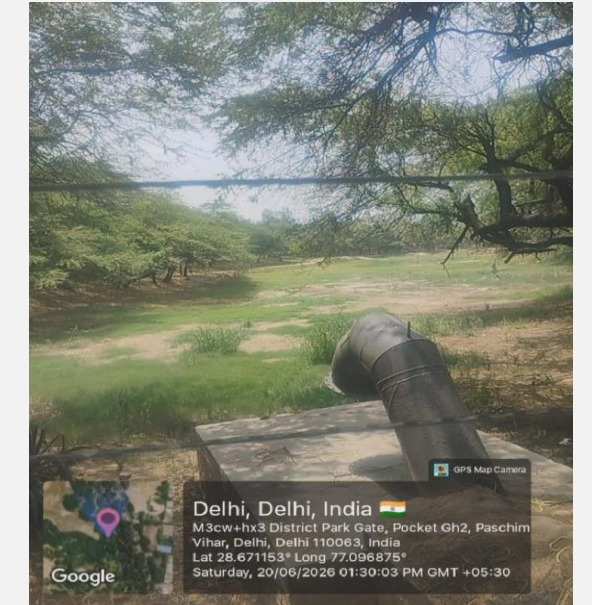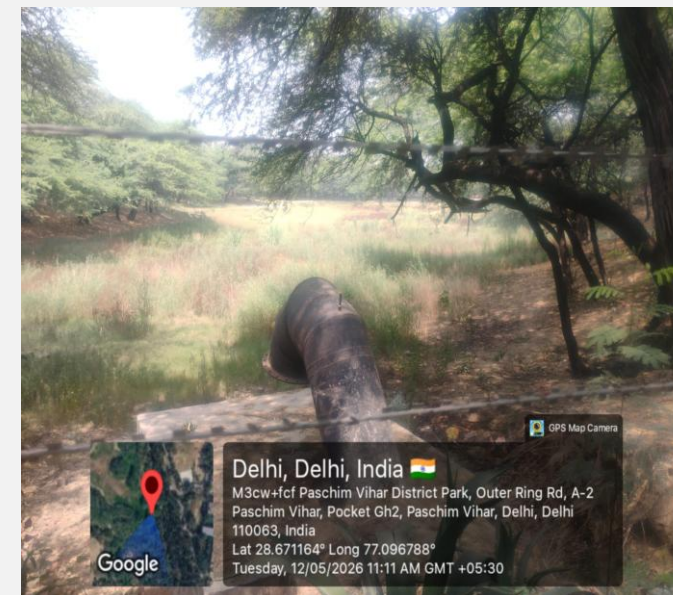

MADIPUR F/74 (PARK AND LAKE AT BHAGWATI TALAB, MADIPUR)

- District: West
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed
- Phase-II- No New work required under Ph-II. However efforts are being made to make the water body perennial.

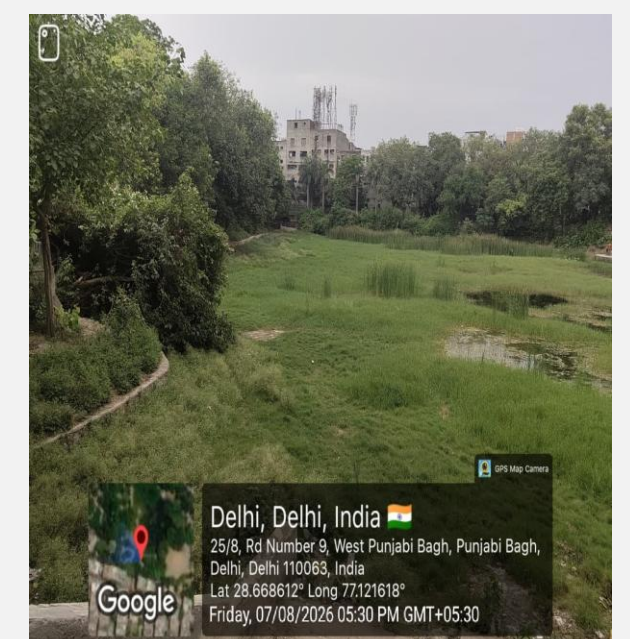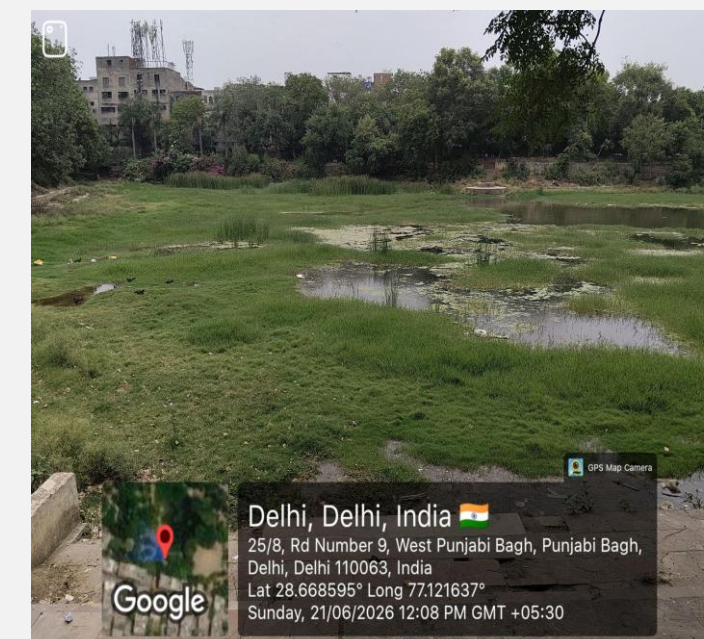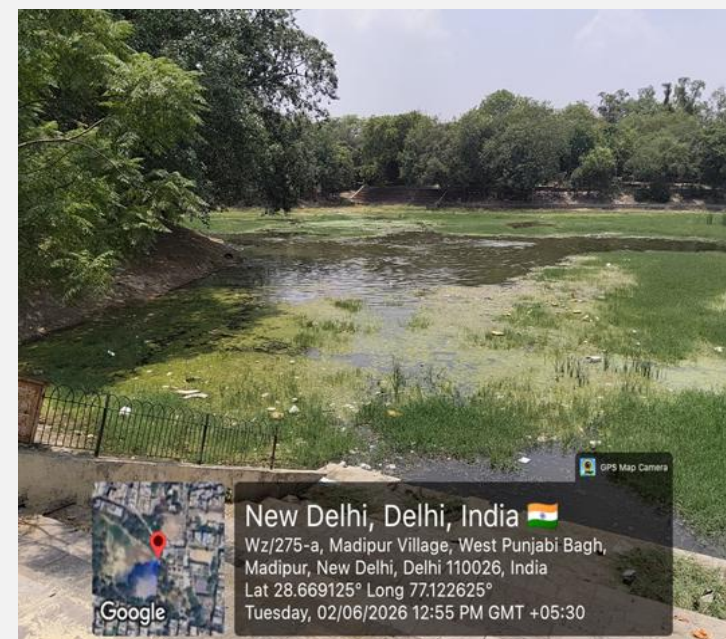

MADIPUR F/75 (PARK AND LAKE AT MADIPUR VILLAGE)

- District: West
- Concerned Officer Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed
- Phase-II- No New work required under Ph-II. However efforts are being made to make the water body perennial.



KILOKARI F/66

- District: South East
- Concerned Officer: Sh. Durga Prasad Chaini 8800432562
- Phase-I- Completed
- Phase-II- hase-I work has been completed and Phase-II work will be completed by 30.10.2026. Phase-II maintenance work i.e. repaire of fencing and gate compelted, site cleaning work and removal of stacked silt from site in progress.





KALINDI AVIRAL (AOL) WATER BODY NO.-2, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer: Sh. Durga Prasad Chaini 8800432562
- Phase-I- Work has been completed
- Phase-II- For Phase-II, the work has been awarded and is currently in progress. It is scheduled to be completed by 31.12.2026.



KALINDI AVIRAL (AOL) WATER BODY NO.-3, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer Sh. Durga Prasad Chaini 8800432562
- Phase-I- Work has been completed
- Phase-II- For Phase-II, the work has been awarded and is currently in progress. It is scheduled to be completed by 31.12.2026.

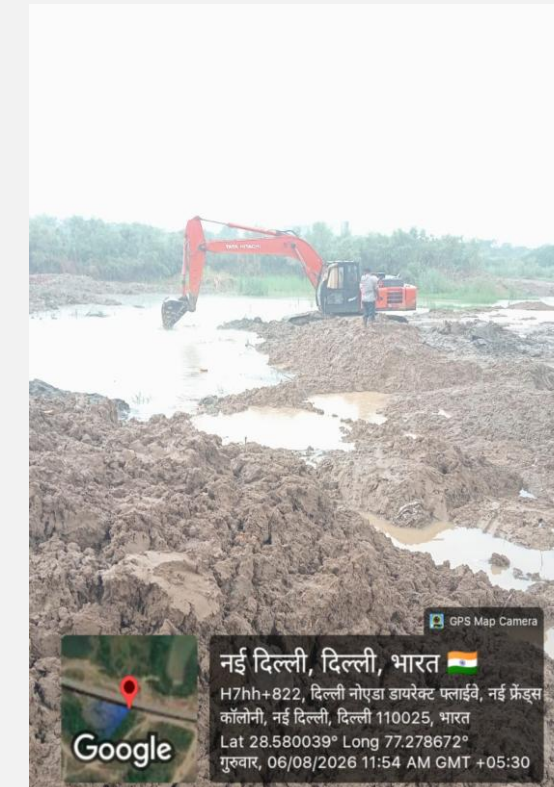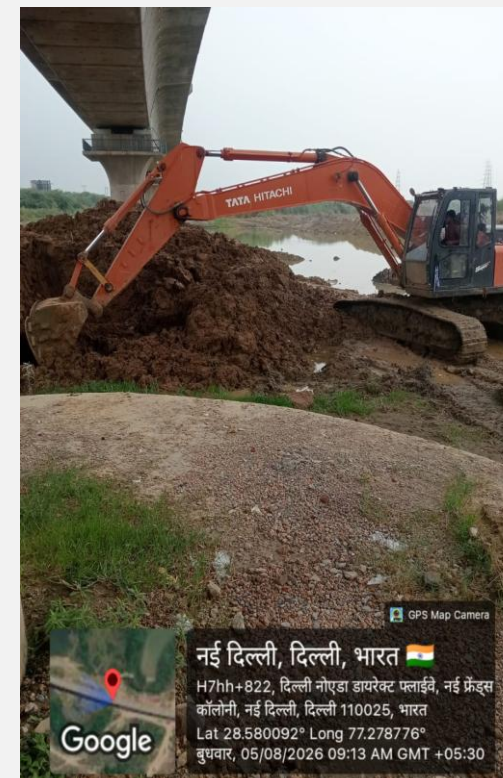




KALINDI AVIRAL (AOL) WATER BODY NO.-4, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer Sh. Durga Prasad Chaini 8800432562
- Phase-I- Work has been completed.
- Phase-II- For Phase-II, the work has been awarded and is currently in progress. It is scheduled to be completed by 31.12.2026.



GHONDA GUJRAN KHADDAR

- District: North East
- Concerned Officer Sh. Sandeep Kushwaha EE/HCD-10 9868915016
- Phase-I- work is completed.
- Phase-II- The work for Phase-2 is not required.

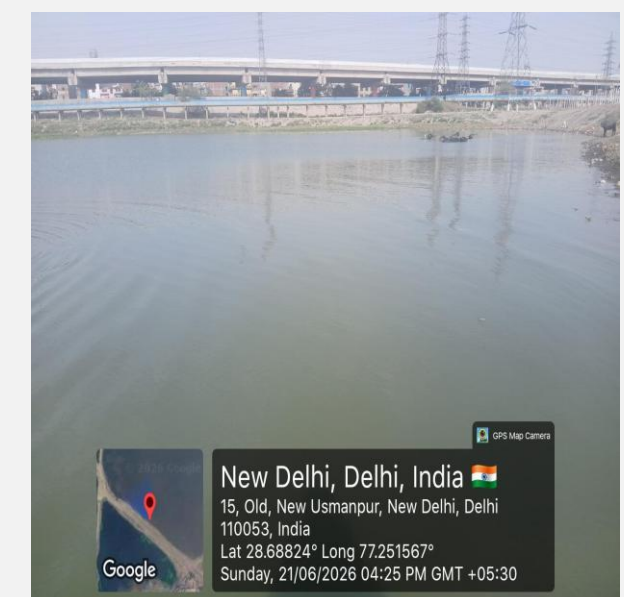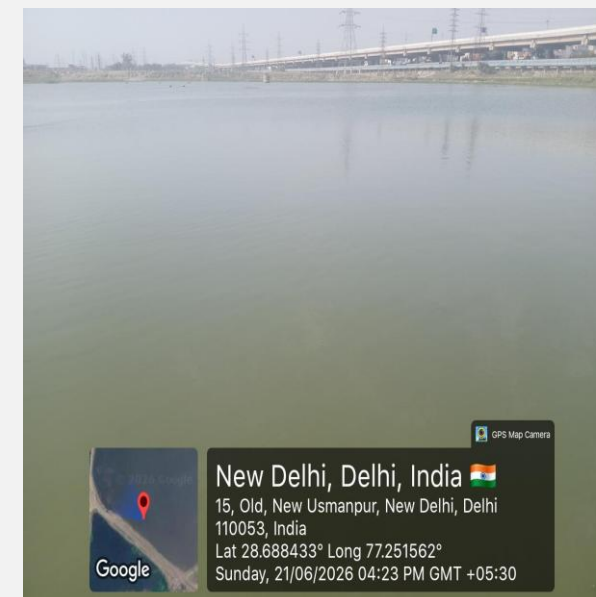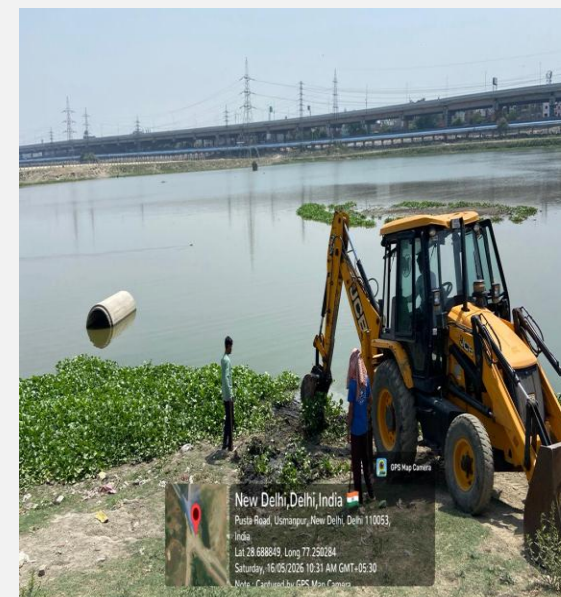


USMANPUR F/89

- District: North East
- Concerned Officer: Sh. Sandeep Kushwaha EE/HCD-10
9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.



K.N. RIDGE KHUNIJHEEL (SERPENTINE LAKE)

- District: North
- Concerned Officer Sh. Sandeep Kushwaha EE/HCD-10
9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.

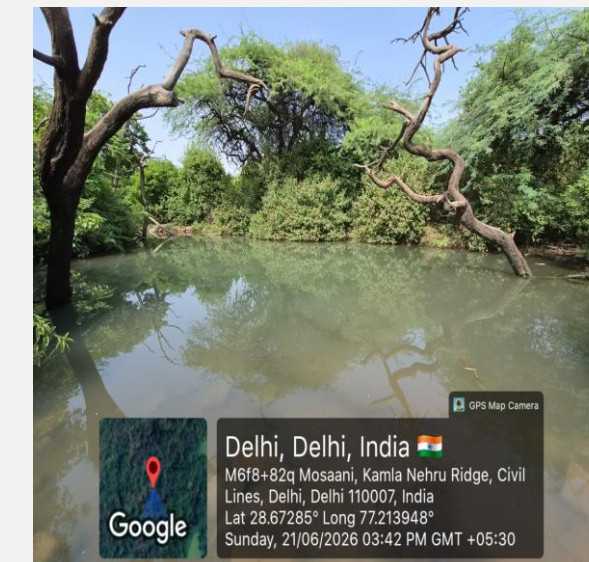



JHARODA MAJRA, BURARI.

- District: North East
- Concerned Officer: Sh. Sandeep Kushwaha EE/HCD-10 9868915016
- Phase-I- Phase-I work is completed. the water from djoining area is coming but watrer is percoleting fastly. Matter is being taking up with DU scientist as the Bio-Diversity park is being looking up by them. Final action for retaing water will be taken accordingly.
- Phase-II- The work for Phase-2 is not required.






TODAPUR (802/800)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026. Phase-I work will be completed by 30-08-2026
- Phase-II- This area/green falls under Reserved Forest Category, therefore no construction activity is allowed in the said park/green . Correspondence with DJB is under progress to provide STP water. However no response has been received from DJB regarding the same.

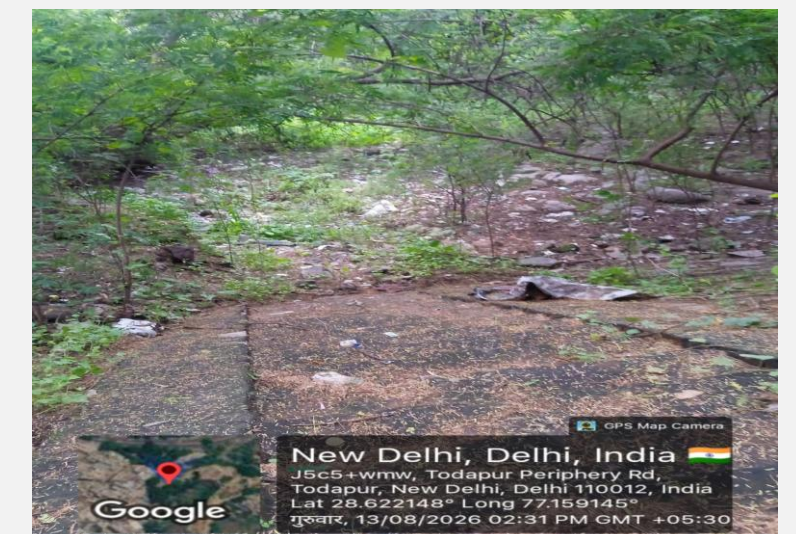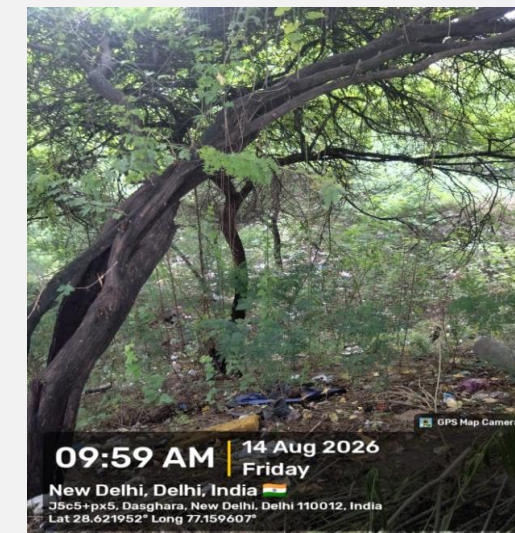



TODAPUR (803/801)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026.Phase-I work will be completed by 30-08-2026
- Phase-II- This area/green falls under Reserved Forest Category, therefore no construction activity is allowed in the said park/green . Correspondence with DJB is under progress to provide STP water. However no response has been received from DJB regarding the same.

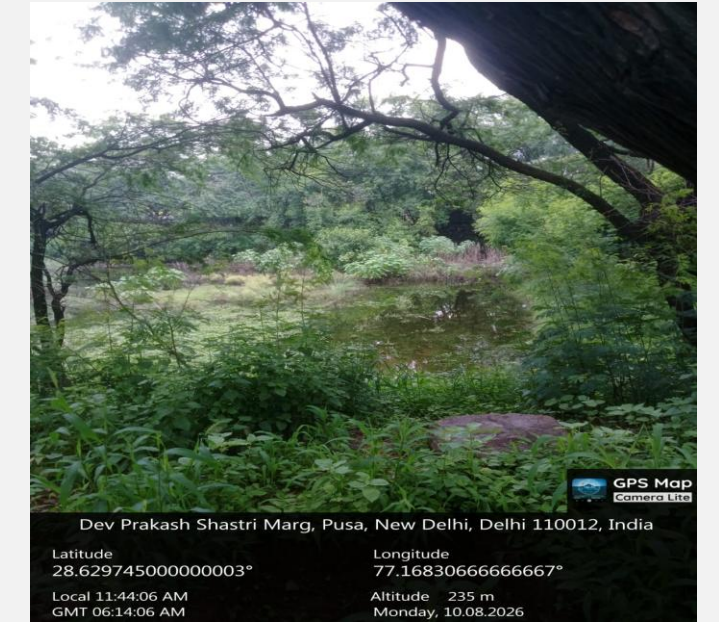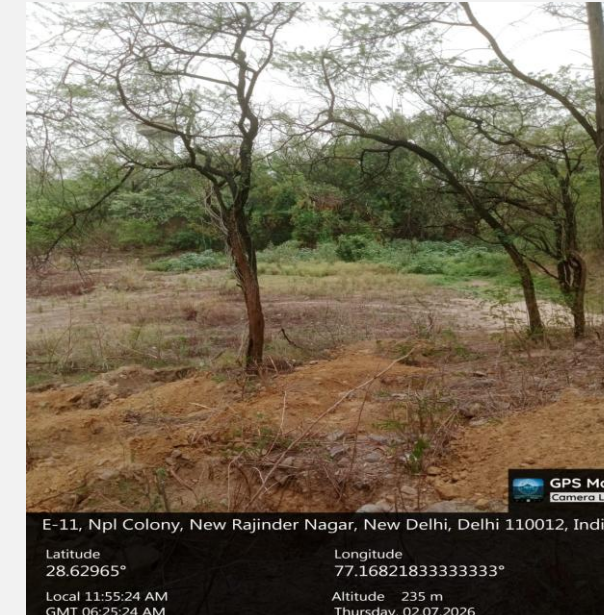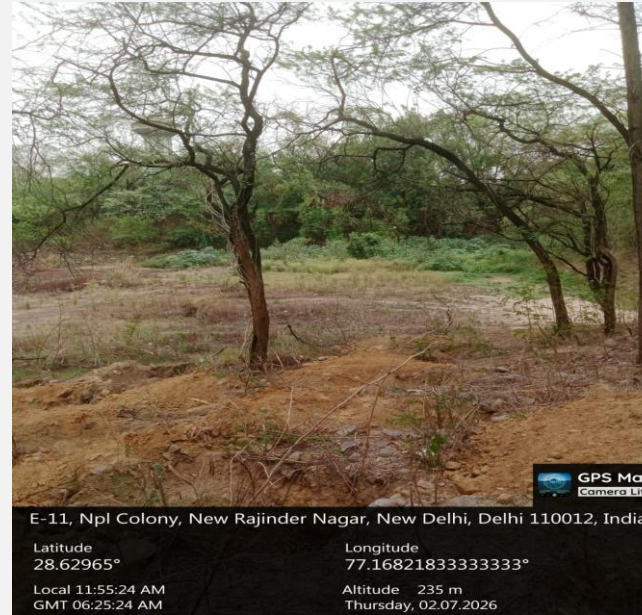



TODAPUR (804/802)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026.Phase-I work will be completed by 30-08-2026
- Phase-II- This area/green falls under Reserved Forest Category, therefore no construction activity is allowed in the said park/green . Correspondence with DJB is under progress to provide STP water. However no response has been received from DJB regarding the same.

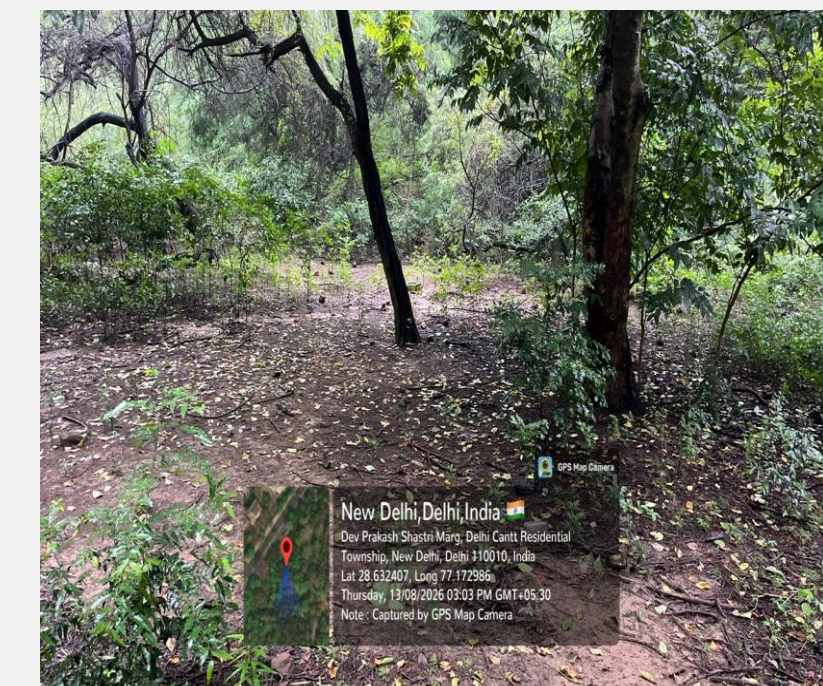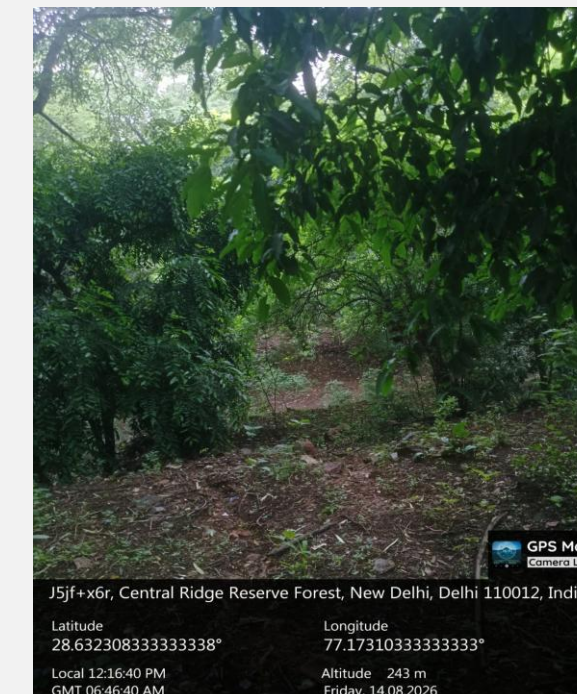

TIHAR LAKE

- District: West
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Works under phase I completed.
- Phase-II- No new work required under Ph-II. However efforts are being made to make the water body perennial.
- CETP water is available at site and a sample was sent for testing of water, COD and other parameters were found substantially high. Proposal for tertiary effluent treatment is being initiated based on the test report.

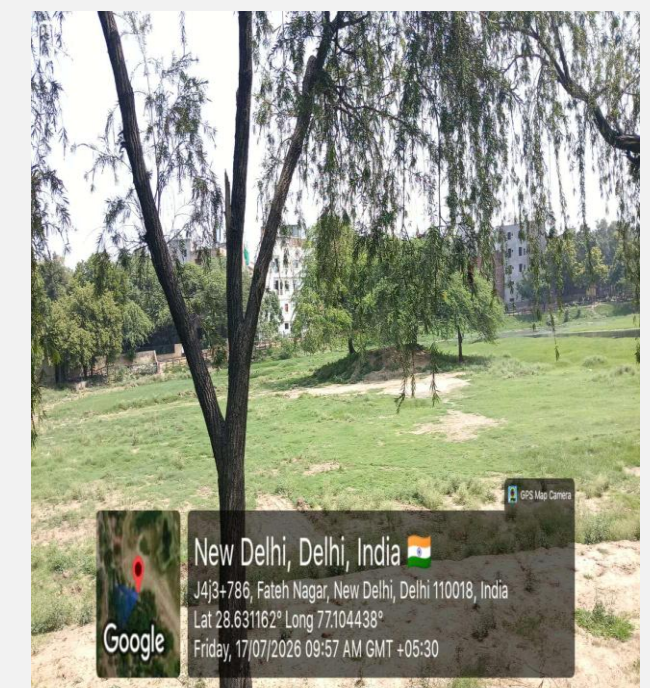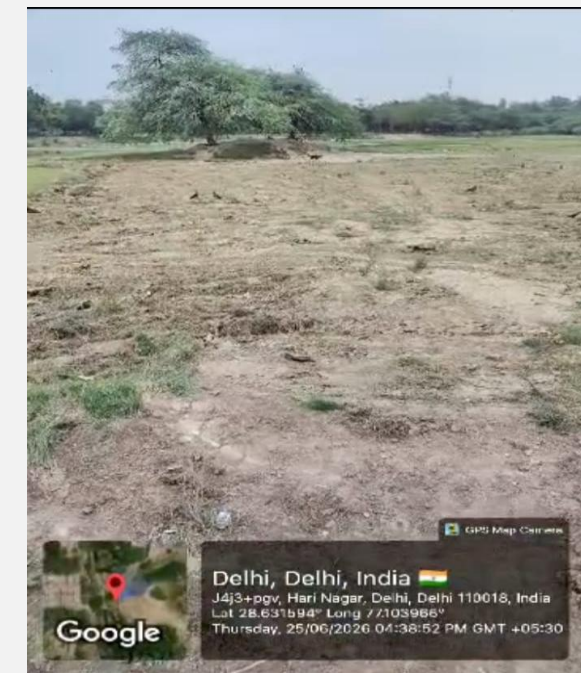

DISTRICT PARK, HARSH VIHAR, PITAMPURA

- District: North West
- Concerned Officer: Sh. Dunni Ram Meena EE/HCD-5 7042737470
- Phase-I- Works under phase I completed.
- Phase-II- The work for Phase-II has been awarded, comprising repair of fencing around the lake, repair of the existing stone pitching and laying of pipelines for channelizing water from the catchment areas into the lake. Works under Phase II will be completed by 31 Dec 2026
- For perennial water supply to maintain the water level in the lake, an estimate has been submitted for A/A & E/S for installation of an STP of 200 KLD capacity. New STP target date 31.05.2027.





DISTRICT PARK AT SECTOR-20, ROHINI (PHASE-3)

- District: North West
- Concerned Officer Sh. Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under Phase- I completed.
- Phase-II- In r/o phase-II it is submitted that necessary infrastructure is available at site except treated water for which necessary coordination is being done with DJB, target date 31.05.2027.




NHP NO. 3 AT SECTOR 23, ROHINI (JHEEL WALA PARK)

- District: North West
- Concerned Officer: Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under Phase- I completed
- .Phase-II- In r/o phase-II it is submitted that necessary infrastructure is available at site.

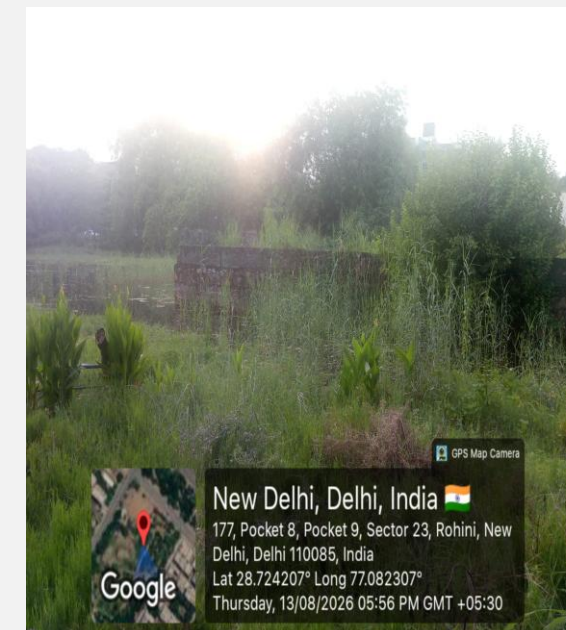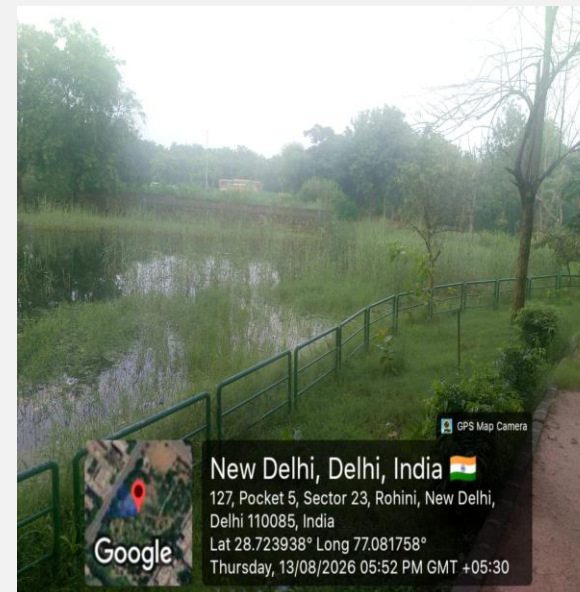



RITHALA F/89 (PARK AND WATER BODY AT RITHALA, SECTOR-5, ROHINI)

- District: North West
- Concerned Officer Sh. Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under phase I completed.
- Phase-II- Works under Phase II , the work of laying the pipeline for collection of rainwater is awarded on 07.09.2026. the work will be completed by 15.10.2026 . necessary correspondence was made by the office of EE/HCD-6 with the concerned offices of DJB seeking permission for extraction of untreated sewage water for installation of High KLD STP. In pursuance thereof, a communication has been received from DJB, wherein permission for extraction of untreated sewage water at Sector-5, Rohini, has been denied.




SUBHASH CAMP BADARPUR

- District: South East
- Concerned Officer: Sh. Saurabh Mishra EE/HCD-2 7054520525
- Phase-I- Restoration of the boundary wall has been completed.
- All works proposed under Phase-I have been completed.
- The waterbody has been properly developed and rejuvenated.
- No desilting is required at present, as the waterbody is in satisfactory condition.
- Phase-II- The civil work proposed under Phase-II have been completed. However, the waterbody is in dry condition.

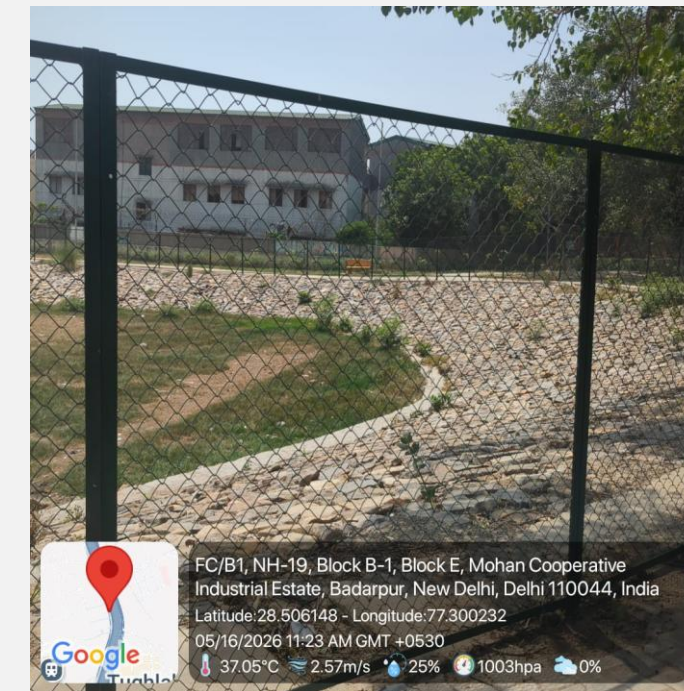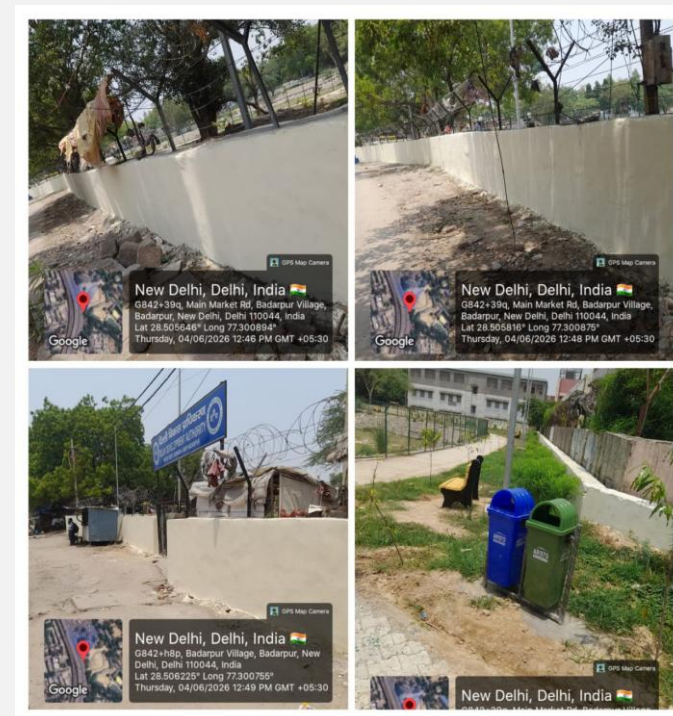



SMRITI VAN NARELA

- District: North
- Concerned Officer Sh. Dunni Ram Meena EE/HCD-5 7042737470
- Phase-I- Works under phase I completed.
- Phase-II- The estimate for Phase-II works, comprising installation of fencing around the lake and laying of pipelines for channelizing water from the catchment areas into the lake, was submitted. A/R & M/O & TS done, NIT yet to be issued by the competent authority. Works under Phase II will be completed by 31 March 2027.
- Perennial water supply for maintaining the water level in the lake is proposed to be provided by the Delhi Jal Board (DJB). Letters have already been written to DJB in this regard (under 200 parks). Water has been supplied by DJB to the lake through a treated water pipeline of DJB passing near the park.

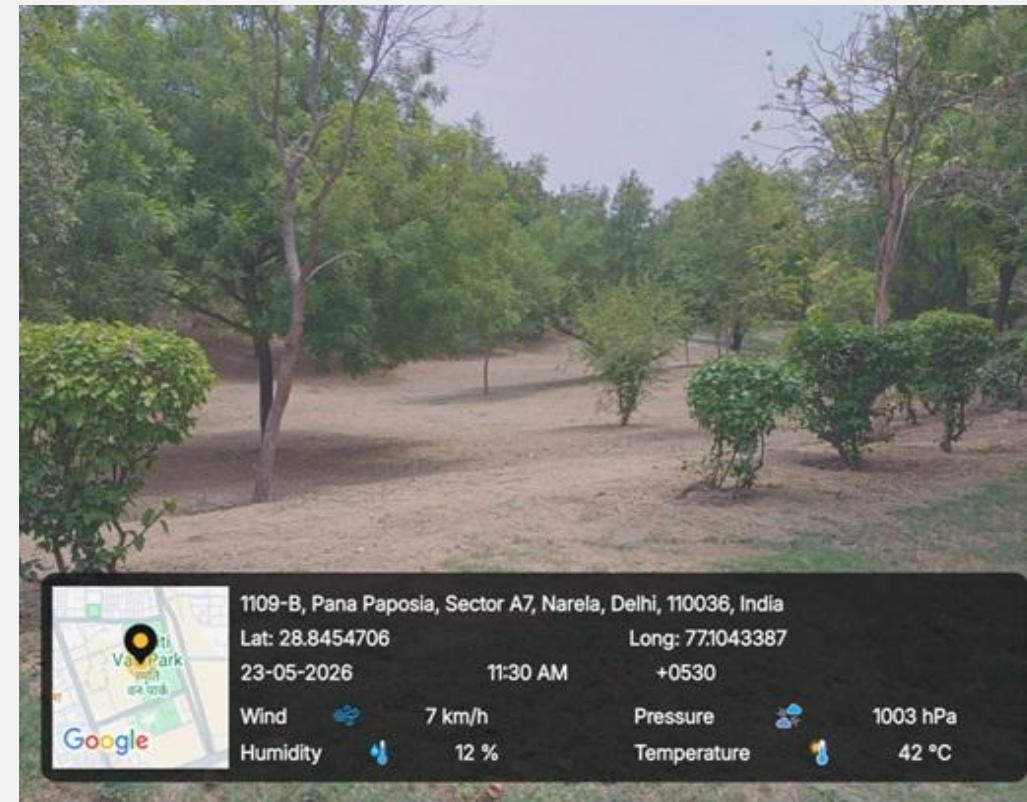

AASTHA KUNJPH-I LL ILL (DISTT. PARK, KALKAJI I/C PARK AROUND KALKAJI TEMPLE) GARHI JHARIA MARIA F/66

- District: South East
- Concerned Officer: Sh. Ashutosh Upadhyay EE/HCD-3 9315869127
- Phase-I:- Work have been completed.
- Phase-II- The estimate for the Phase-II works, comprising installation of fencing around the lake, provision of signage boards, laying of pipelines for channelizing water from the catchment areas into the lake, and other miscellaneous works, has been sanctioned and the tender has been floated. The works under Phase-II shall be completed by the end of January 2027.
- The preliminary estimate for supply of water through the STP under Phase-II has been submitted and the necessary statutory approvals are being obtained from the concerned departments. The work shall be completed within 180 days from the date of award of the work. Accordingly, the tentative date of completion of the works envisaged under Phase-II is 30.04.2027.

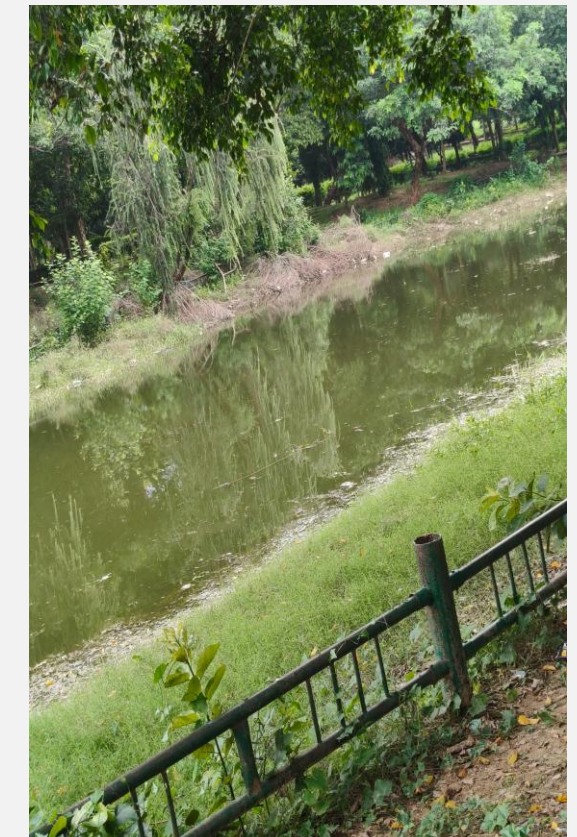

BHALSWA JAHANGIRPURI, BEHIND SANJAY ENCLAVE

- District: North West
- Concerned Officer: Sh. Dunni Ram Meena EE/HCD-5
Mob 7042737470
- Phase-I- Works under phase I completed.
- Phase-II: Tender has been awarded to execute work under phase II such as installation of RCC pipes to collect rain water from submerged area & construction of collection chambers, installation of GI pipe railing around the lake and installation of board. Work is under progress.
- Perennial water supply for maintaining the water level in the lake is proposed to be provided by the Delhi Jal Board (DJB). Letters have already been written to DJB in this regard (under 200 parks).

